

LitPath AI: Smart Pathfinder for Theses and Dissertations

Group 06 HecTech

Project Management
PROJMAN MI231

Mr. Jose Eugenio L. Quesada

OUR TEAM



Mr. Gonzalo V. Gumogda
Project Adviser



Cempron, Charijoy



Sta Ana, Joshua



Dulay, Jenine Elaine



Tomon, Tracie

Table of Contents

1 Agile Scrum Ceremonies

2 Agile Scrum Documents

3 PMBOK: Initiation Phase

4 PMBOK: Planning Phase

5 System Design Document

5 PMBOK: Monitoring and Controlling Phase

5 PMBOK: Closing Phase

6 Costs


7 OpenProject

8 Demo

AGILE SCRUM CEREMONIES

Agile Scrum Ceremonies

Sprint 2 Backlogs

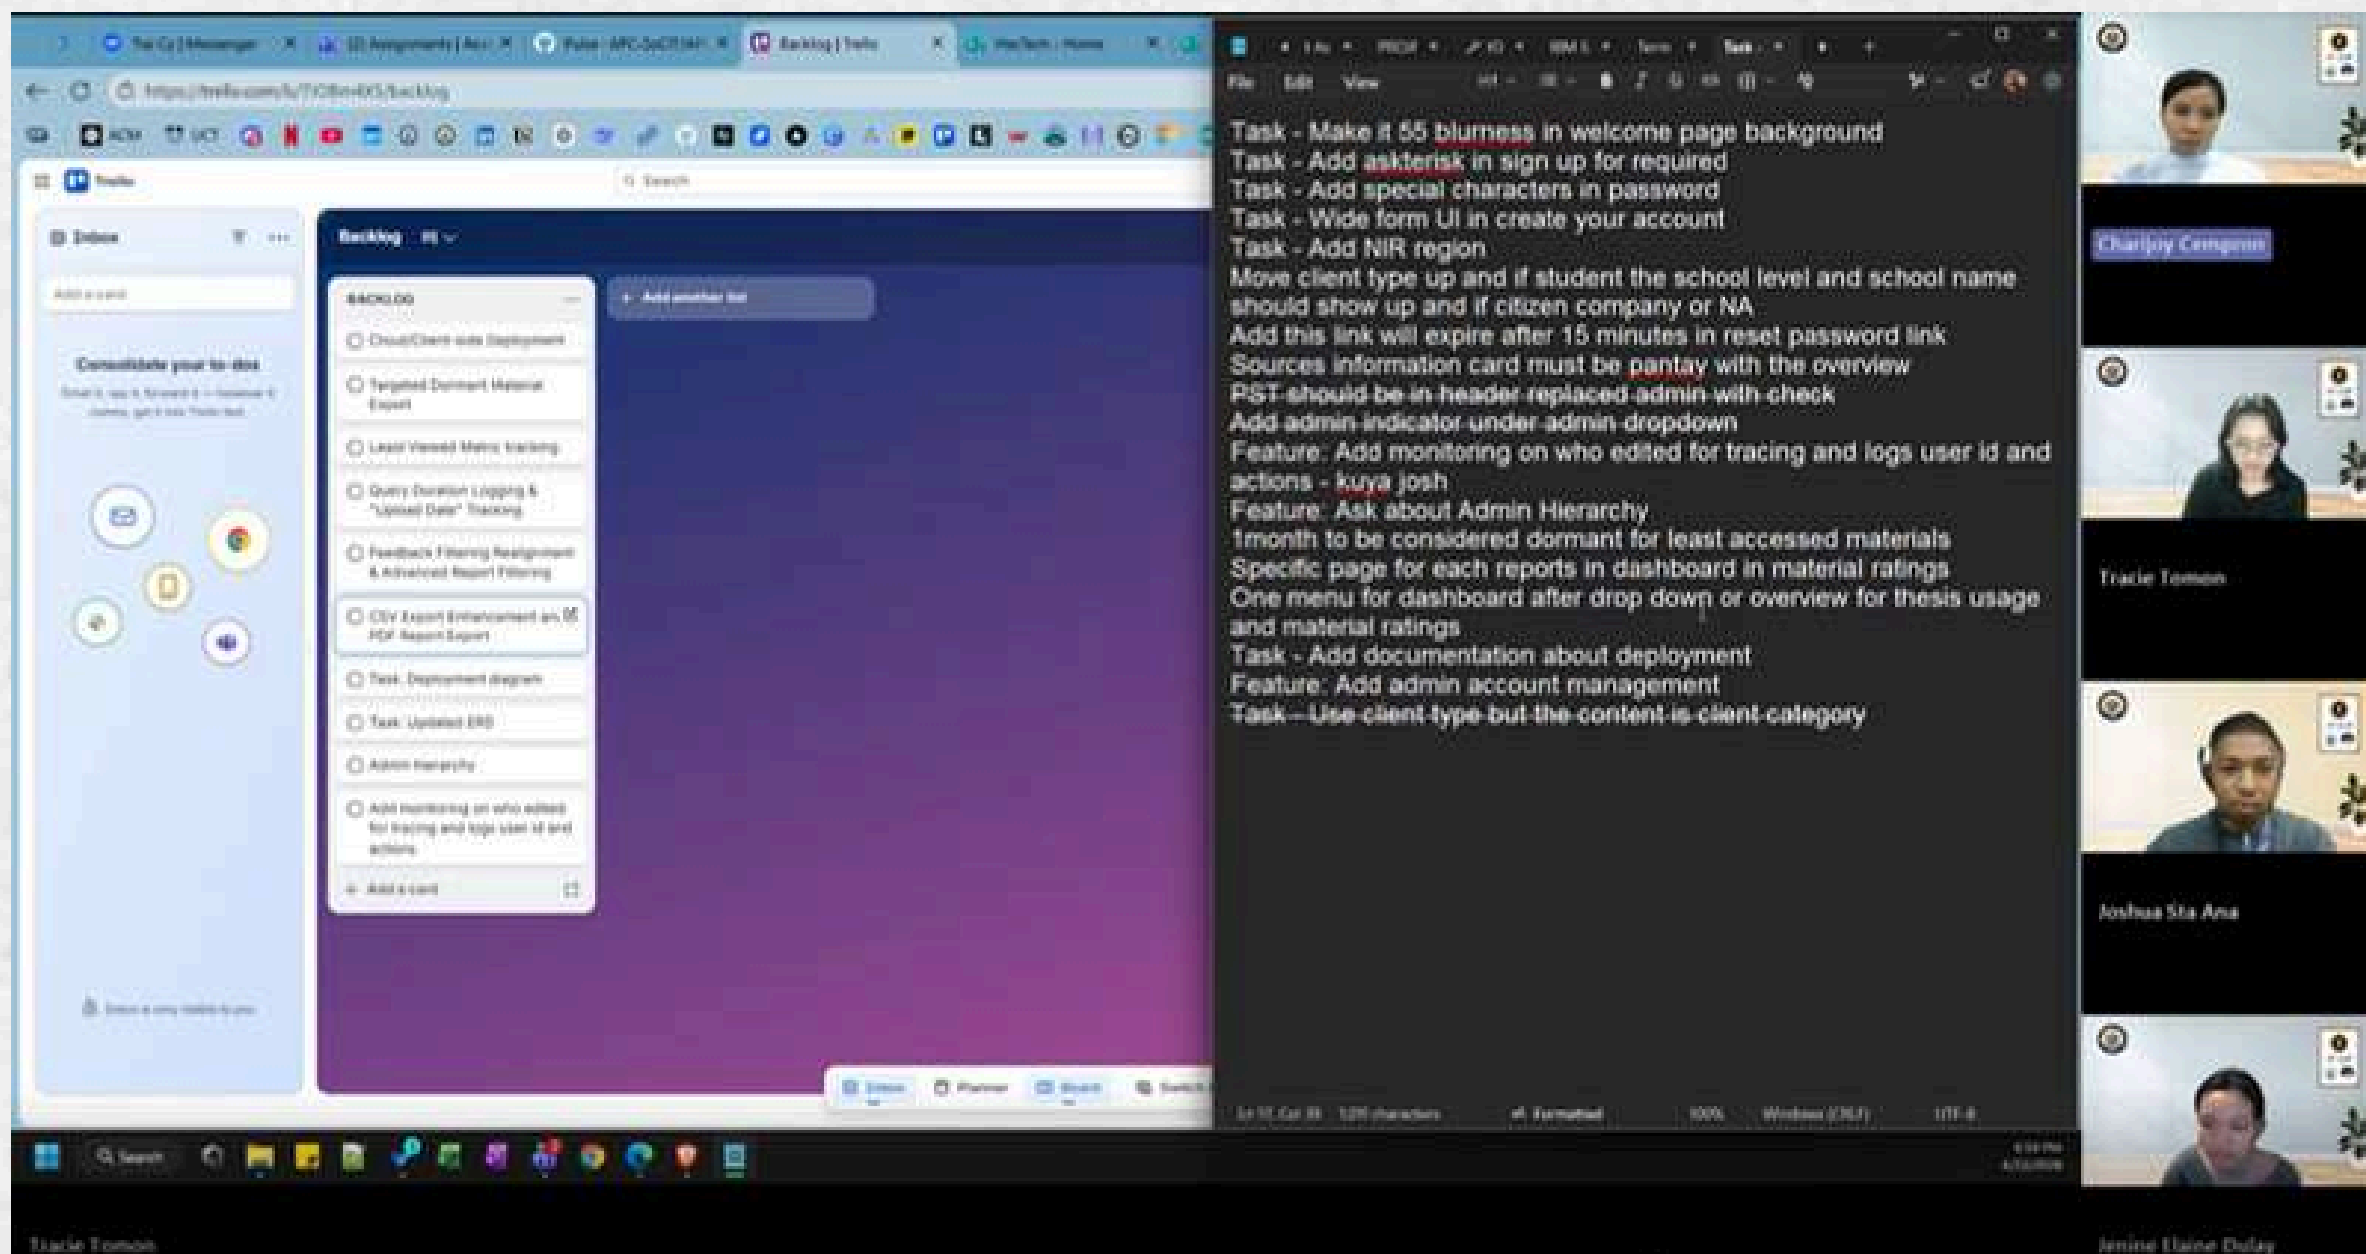

Backlog

- CloudClient side Deployment
- Targeted Dormant Material Export
- Least Viewed Metric tracking
- Query Duration Logging & "Upload Date" Tracking
- Feedback Filtering Realignment & Advanced Report Filtering
- CSV Export Enhancement and PDF Report Export
- Task: Deployment diagram
- Task: Updated ERD
- Admin Hierarchy
- Add monitoring on who edited for tracing and logs user id and actions

Tasks:

- Task - Make it 55 blumess in welcome page background
- Task - Add asterisk in sign up for required
- Task - Add special characters in password
- Task - Wide form UI in create your account
- Task - Add NIR region
- Move client type up and if student the school level and school name should show up and if citizen company or NA
- Add this link will expire after 15 minutes in reset password link
- Sources information card must be pantay with the overview
- PST should be in header-replaced-admin-with-check
- Add admin-indicator under admin-dropdown
- Feature: Add monitoring on who edited for tracing and logs user id and actions - kuya josh
- Feature: Ask about Admin Hierarchy
- 1month to be considered dormant for least accessed materials
- Specific page for each reports in dashboard in material ratings
- One menu for dashboard after drop down or overview for thesis usage and material ratings
- Task - Add documentation about deployment
- Feature: Add admin account management
- Task - Use client-type-but-the-content-is-client-category

Participants:

- Charjoey Cernigoi
- Tracie Tomon
- Joshua Sta Ana
- Jennine Elaine Bulag


1.12 AY 2025-2026 T3 Sprint 02	15	177 points
04/22/2026 - 05/09/2026		
FEATURE #6526 Closed	0 points	
Feature 12.0 Targeted Dormant Material Export		
USER STORY #6702 Closed	20 points	
As a Librarian Administrator, I want to export a targeted list of dormant materials (not accessed for 1 month) from the LitPath AI dashboard, so that I can review and manage underperforming thesis and dissertation content efficiently.		
FEATURE #6527 Closed	0 points	
Feature 13.0 Least Viewed Metric tracking		
USER STORY #6704 Closed	18 points	
As a Librarian Administrator, I want to view a Least Viewed Materials metric in the Material Rating tab replacing the Top Least Accessed metric, so that I can better track and identify underperforming thesis and dissertation content in LitPath AI.		
FEATURE #6514 Closed	0 points	
Feature 14.0 Query Duration Logging & "Upload Date" Tracking		
USER STORY #6804 Closed	23 points	
As an admin, I want the system to automatically log how long each user stays in a session so that I can monitor user engagement and activity.		
USER STORY #6805 Closed	16 points	
As an admin, I want the upload date of each material to be automatically recorded so that I can track when it was added to the system.		
FEATURE #6515 Closed	0 points	
Feature 15.0 Feedback Filtering Realignment & Advanced Report Filtering		
USER STORY #6796 Closed	22 points	
As a Librarian Administrator, I want to filter feedback records by Category and Status, So that I can quickly isolate specific subsets of feedback data and generate focused reports without manually scanning through unrelated entries.		
FEATURE #6516 Closed	0 points	
Feature 16.0 CSV Export Enhancement and PDF Report Export		
USER STORY #6801 Closed	20 points	
As a Library Administrator, I want to export feedback data to CSV or PDF based on the filters I've applied, so the file only includes the specific data I need and not the entire dataset.		
FEATURE #6524 Closed	0 points	
Feature 17.0 Admin Hierarchy		
USER STORY #6640 Closed	32 points	
As an IT Administrator, I want to define and manage a hierarchy of admin roles (IT Administrator and Librarian Administrator) with specific permissions so that each role can securely and efficiently perform their responsibilities within LitPath AI.		
FEATURE #6525 Closed	0 points	
Feature 18.0 Add monitoring on who edited for tracing and logs user id and actions		
USER STORY #6838 Closed	26 points	
As a Librarian Administrator, I want to track and log who reviews and validates user feedback (including user ID and actions taken) so that we can ensure accountability, trace changes, and maintain transparency.		

Tomon, Tracie



Agile Scrum Ceremonies

Sprint 2 Planning meeting

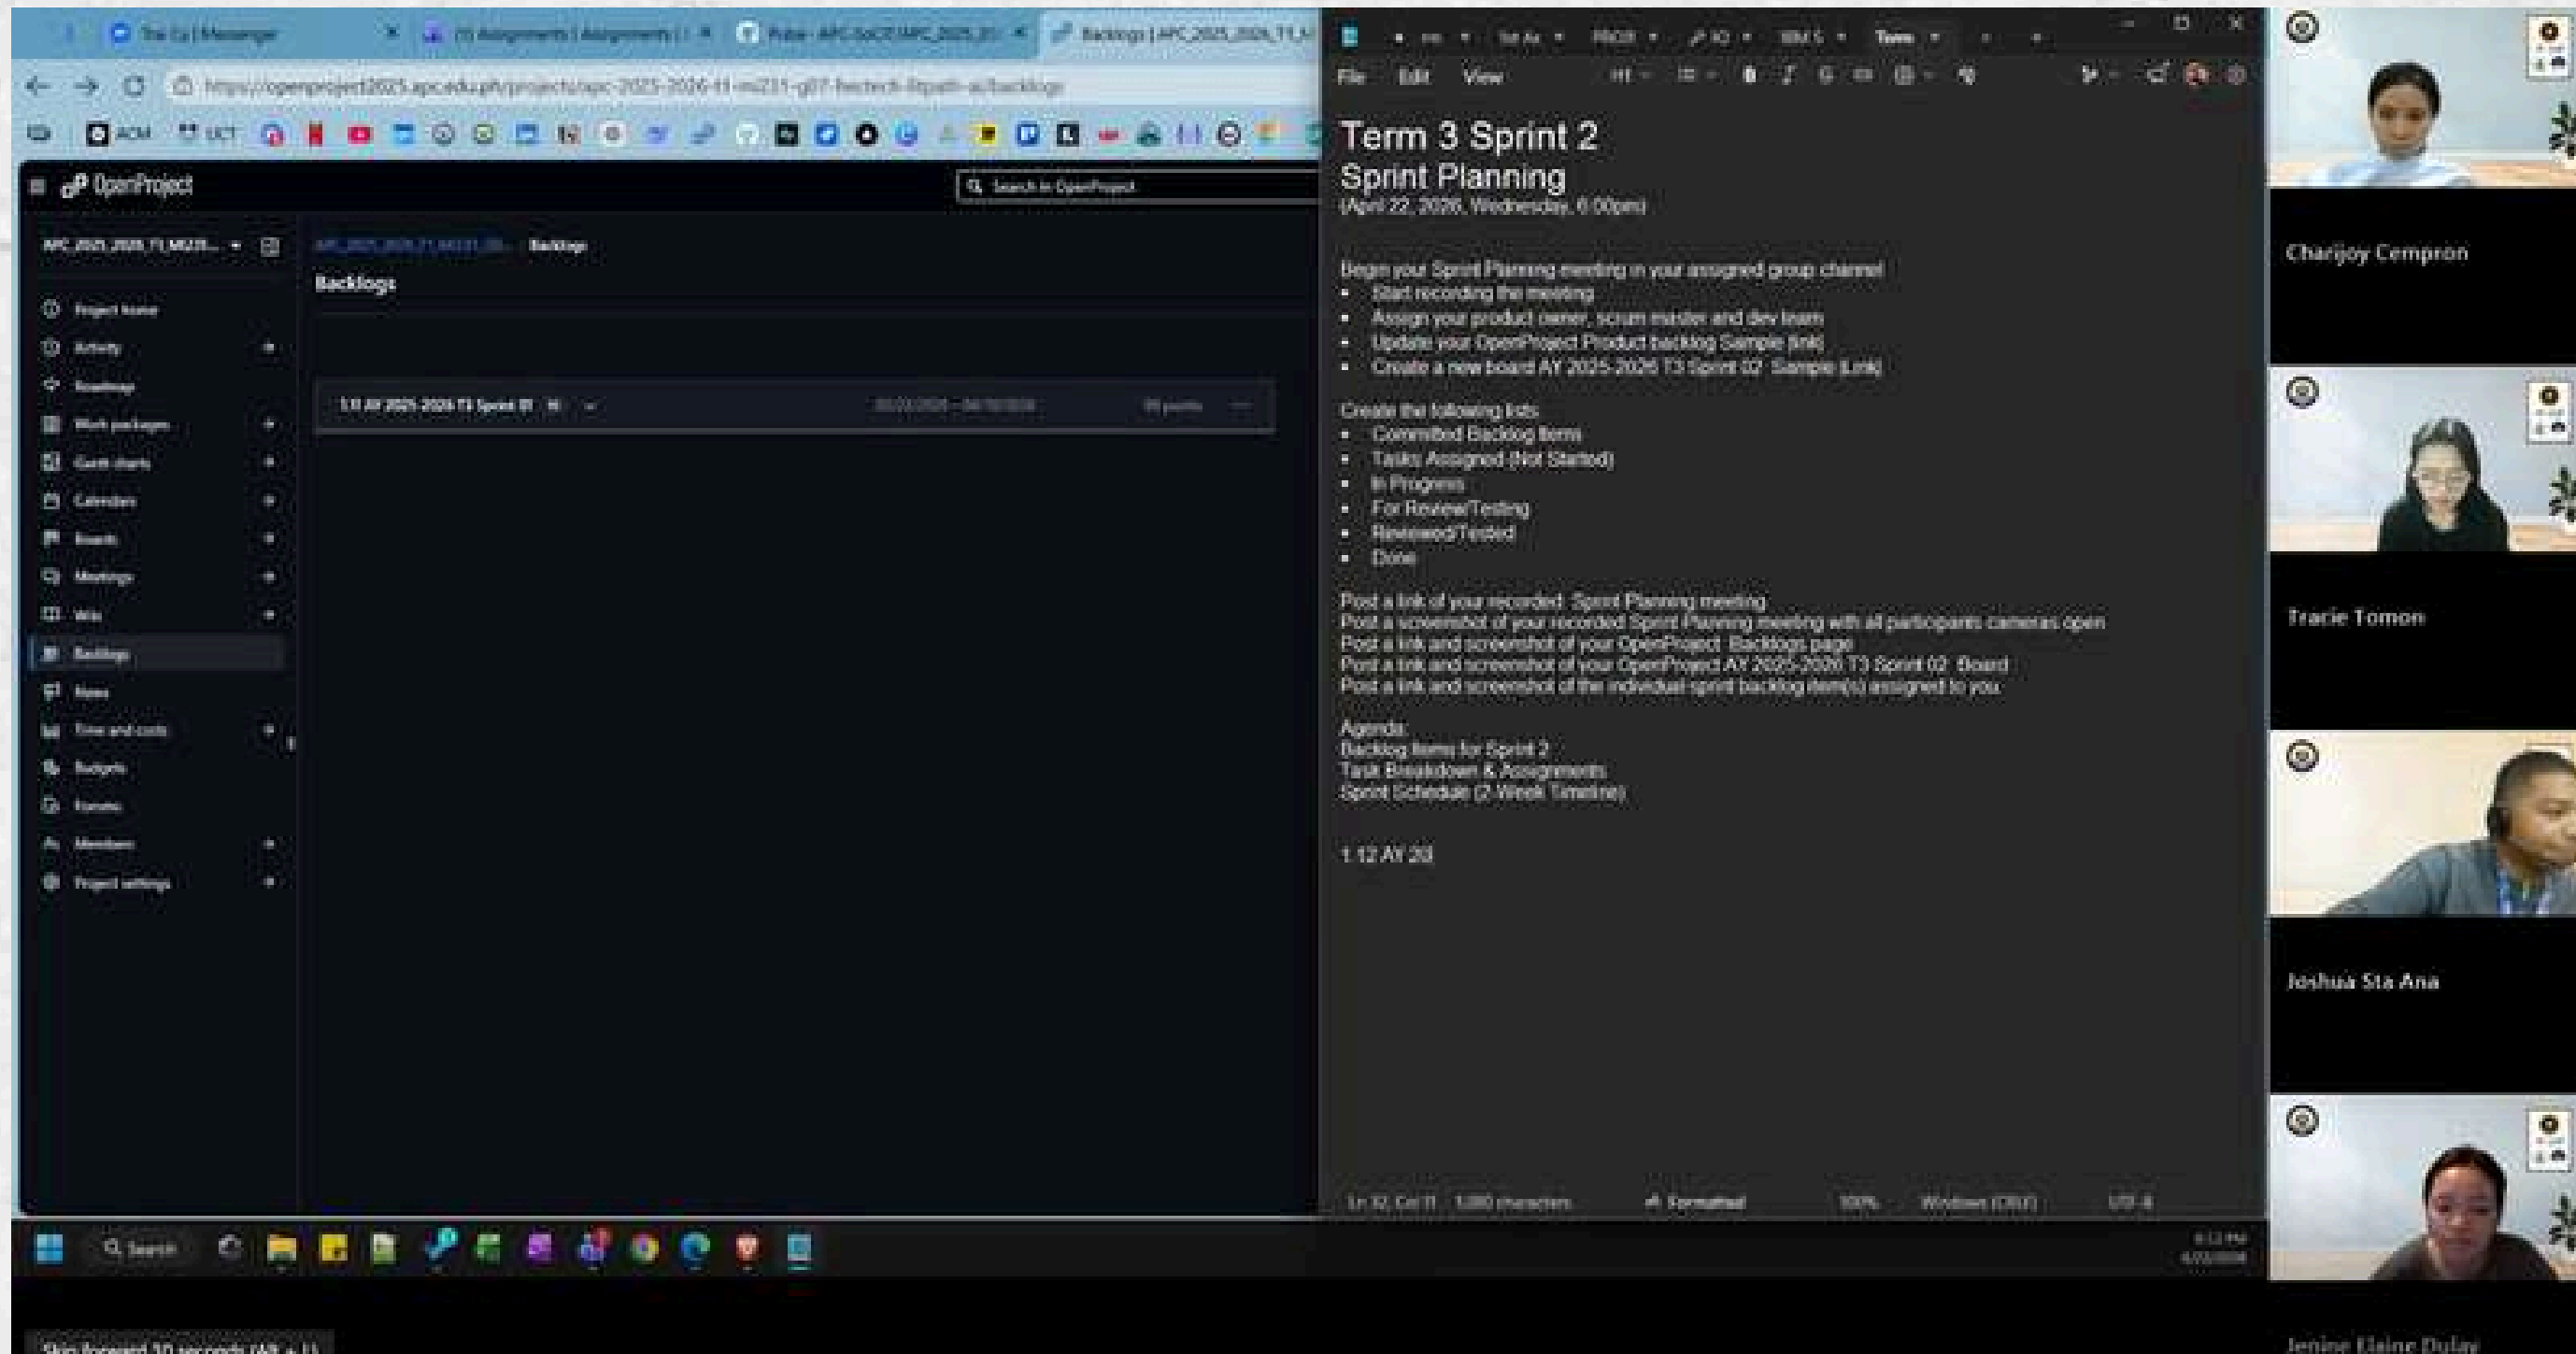

The screenshot displays a Zoom meeting interface. The main window shows a screen share of the OpenProject Backlog for 'Term 3 Sprint 2 Sprint Planning' (April 22, 2026, Wednesday, 6:00pm). The OpenProject interface includes a sidebar with navigation options like Project Name, Activity, Backlog, Work packages, Gantt chart, Calendar, Board, Meetings, and Wiki. The main content area shows the Backlog with a table of items. The Zoom meeting title bar indicates 'Term 3 Sprint 2 Sprint Planning' and 'April 22, 2026, Wednesday, 6:00pm'. The meeting content includes instructions for the Sprint Planning meeting, a list of tasks to be created (Committed Backlog items, Tasks Assigned (Not Started), In Progress, For Review/Testing, Reviewed/Testing, Done), and an agenda for the meeting. The participants list on the right side of the Zoom window includes Charlijoy Cempron, Tracie Tomon, Joshua Sia Ana, and Jenine Elaine Dula.

Term 3 Sprint 2 Sprint Planning
(April 22, 2026, Wednesday, 6:00pm)

Begin your Sprint Planning meeting in your assigned group channel

- Start recording the meeting
- Assign your product owner, scrum master and dev team
- Update your OpenProject Product backlog (Sample Link)
- Create a new board AY 2025-2026 T3 Sprint 02 Sample (Link)

Create the following tabs

- Committed Backlog items
- Tasks Assigned (Not Started)
- In Progress
- For Review/Testing
- Reviewed/Testing
- Done

Post a link of your recorded Sprint Planning meeting
Post a screenshot of your recorded Sprint Planning meeting with all participants cameras open
Post a link and screenshot of your OpenProject Backlog page
Post a link and screenshot of your OpenProject AY 2025-2026 T3 Sprint 02 Board
Post a link and screenshot of the individual sprint backlog item(s) assigned to you

Agenda:
Backlog items for Sprint 2
Task Breakdown & Assignments
Sprint Schedule (2-Week Timeline)

1:12 AM '26



Participants: Charlijoy Cempron, Tracie Tomon, Joshua Sia Ana, Jenine Elaine Dula

Tomon, Tracie



Agile Scrum Ceremonies

Daily Stand-Up

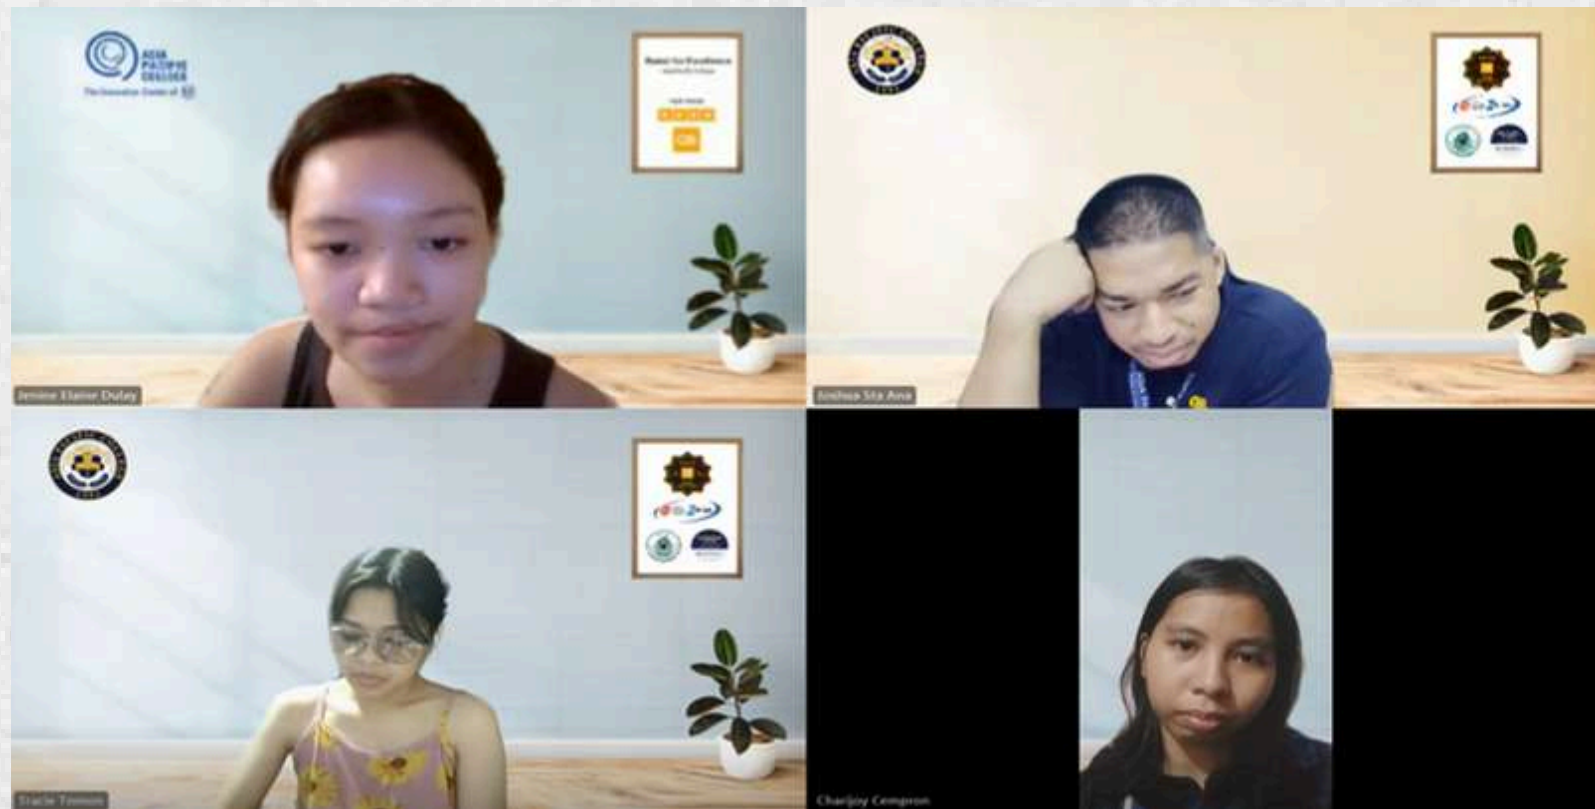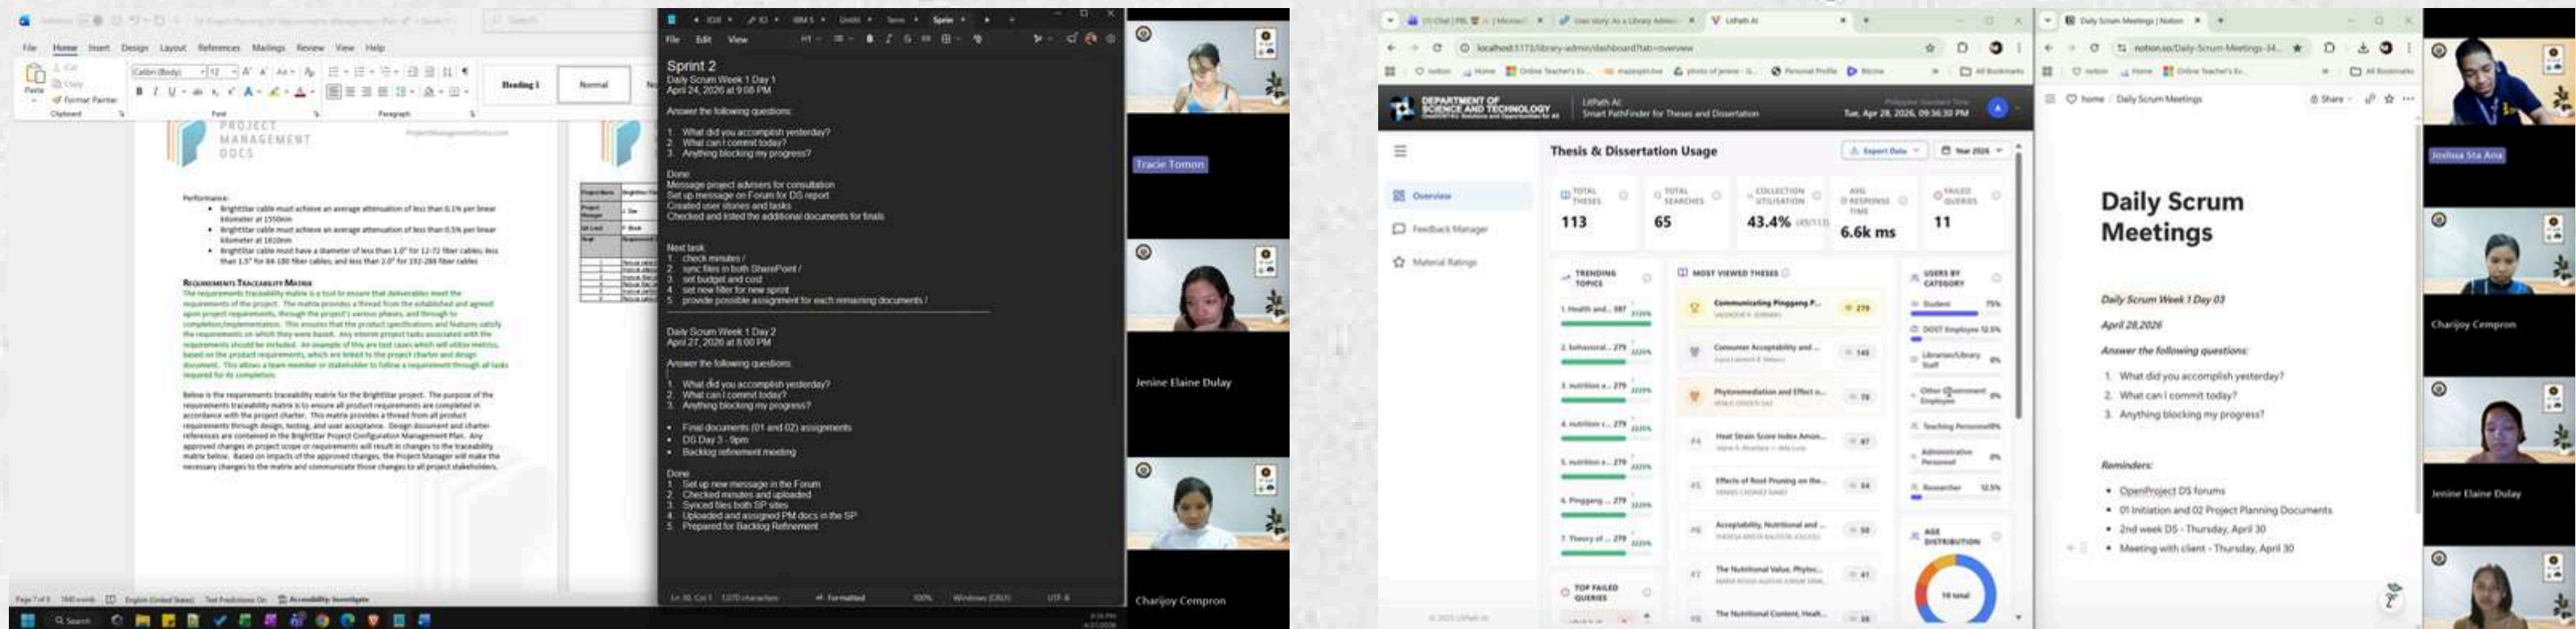


Tomon, Tracie



Agile Scrum Ceremonies

Sprint 2 Backlog Refinement meeting

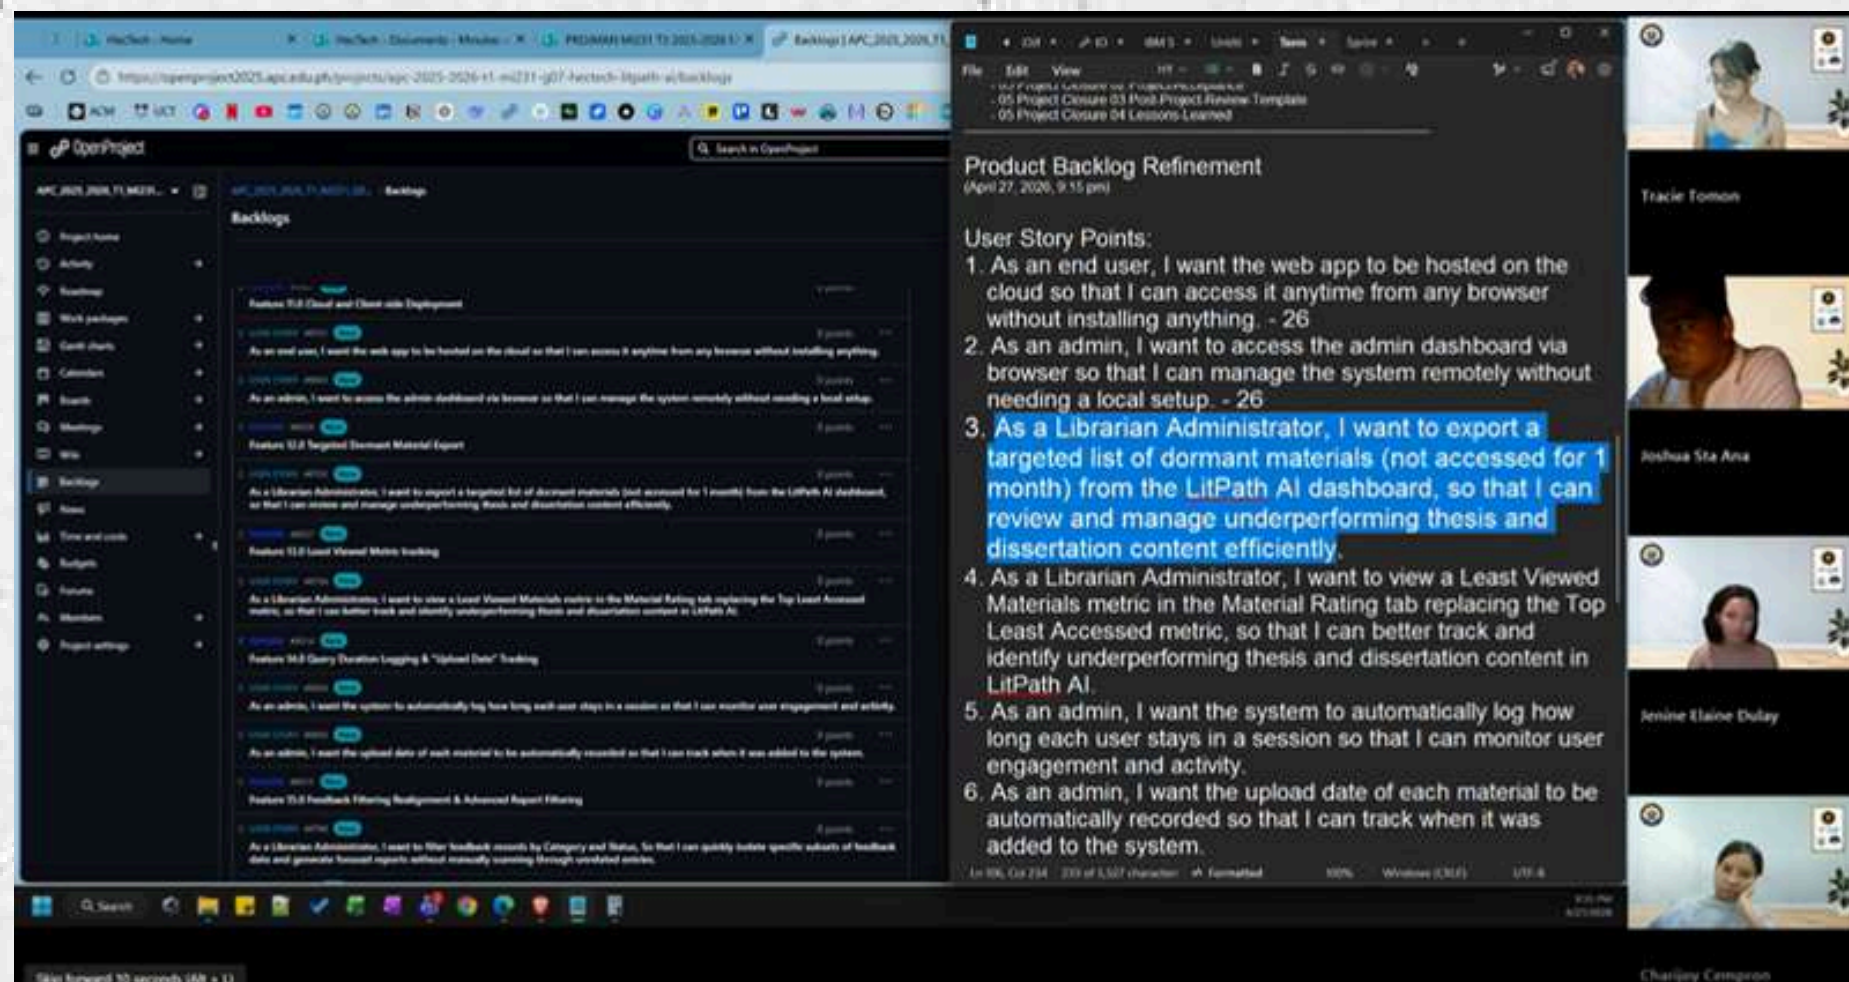

Product Backlog Refinement
(April 27, 2026, 9:15 pm)

User Story Points:


1. As an end user, I want the web app to be hosted on the cloud so that I can access it anytime from any browser without installing anything. - 26
2. As an admin, I want to access the admin dashboard via browser so that I can manage the system remotely without needing a local setup. - 26
3. As a Librarian Administrator, I want to export a targeted list of dormant materials (not accessed for 1 month) from the LitPath AI dashboard, so that I can review and manage underperforming thesis and dissertation content efficiently.
4. As a Librarian Administrator, I want to view a Least Viewed Materials metric in the Material Rating tab replacing the Top Least Accessed metric, so that I can better track and identify underperforming thesis and dissertation content in LitPath AI.
5. As an admin, I want the system to automatically log how long each user stays in a session so that I can monitor user engagement and activity.
6. As an admin, I want the upload date of each material to be automatically recorded so that I can track when it was added to the system.

1.12 AY 2025-2026 T3 Sprint 02	15	177 points	...
04/22/2026 - 05/09/2026			
FEATURE #6526	Closed	0 points	...
Feature 12.0 Targeted Dormant Material Export			
USER STORY #6702	Closed	20 points	...
As a Librarian Administrator, I want to export a targeted list of dormant materials (not accessed for 1 month) from the LitPath AI dashboard, so that I can review and manage underperforming thesis and dissertation content efficiently.			
FEATURE #6527	Closed	0 points	...
Feature 13.0 Least Viewed Metric tracking			
USER STORY #6704	Closed	18 points	...
As a Librarian Administrator, I want to view a Least Viewed Materials metric in the Material Rating tab replacing the Top Least Accessed metric, so that I can better track and identify underperforming thesis and dissertation content in LitPath AI.			
FEATURE #6514	Closed	0 points	...
Feature 14.0 Query Duration Logging & "Upload Date" Tracking			
USER STORY #6804	Closed	23 points	...
As an admin, I want the system to automatically log how long each user stays in a session so that I can monitor user engagement and activity.			
USER STORY #6805	Closed	16 points	...
As an admin, I want the upload date of each material to be automatically recorded so that I can track when it was added to the system.			
FEATURE #6515	Closed	0 points	...
Feature 15.0 Feedback Filtering Realignment & Advanced Report Filtering			
USER STORY #6796	Closed	22 points	...
As a Librarian Administrator, I want to filter feedback records by Category and Status, so that I can quickly isolate specific subsets of feedback data and generate focused reports without manually scanning through unrelated entries.			
FEATURE #6516	Closed	0 points	...
Feature 16.0 CSV Export Enhancement and PDF Report Export			
USER STORY #6801	Closed	20 points	...
As a Library Administrator, I want to export feedback data to CSV or PDF based on the filters I've applied, so the file only includes the specific data I need and not the entire dataset.			
FEATURE #6524	Closed	0 points	...
Feature 17.0 Admin Hierarchy			
USER STORY #6640	Closed	32 points	...
As an IT Administrator, I want to define and manage a hierarchy of admin roles (IT Administrator and Librarian Administrator) with specific permissions so that each role can securely and efficiently perform their responsibilities within LitPath AI.			
FEATURE #6525	Closed	0 points	...
Feature 18.0 Add monitoring on who edited for tracing and logs user id and actions			
USER STORY #6638	Closed	26 points	...
As a Librarian Administrator, I want to track and log who reviews and validates user feedback (including user ID and actions taken) so that we can ensure accountability, trace changes, and maintain transparency.			



Agile Scrum Ceremonies

Sprint 2 Review meeting

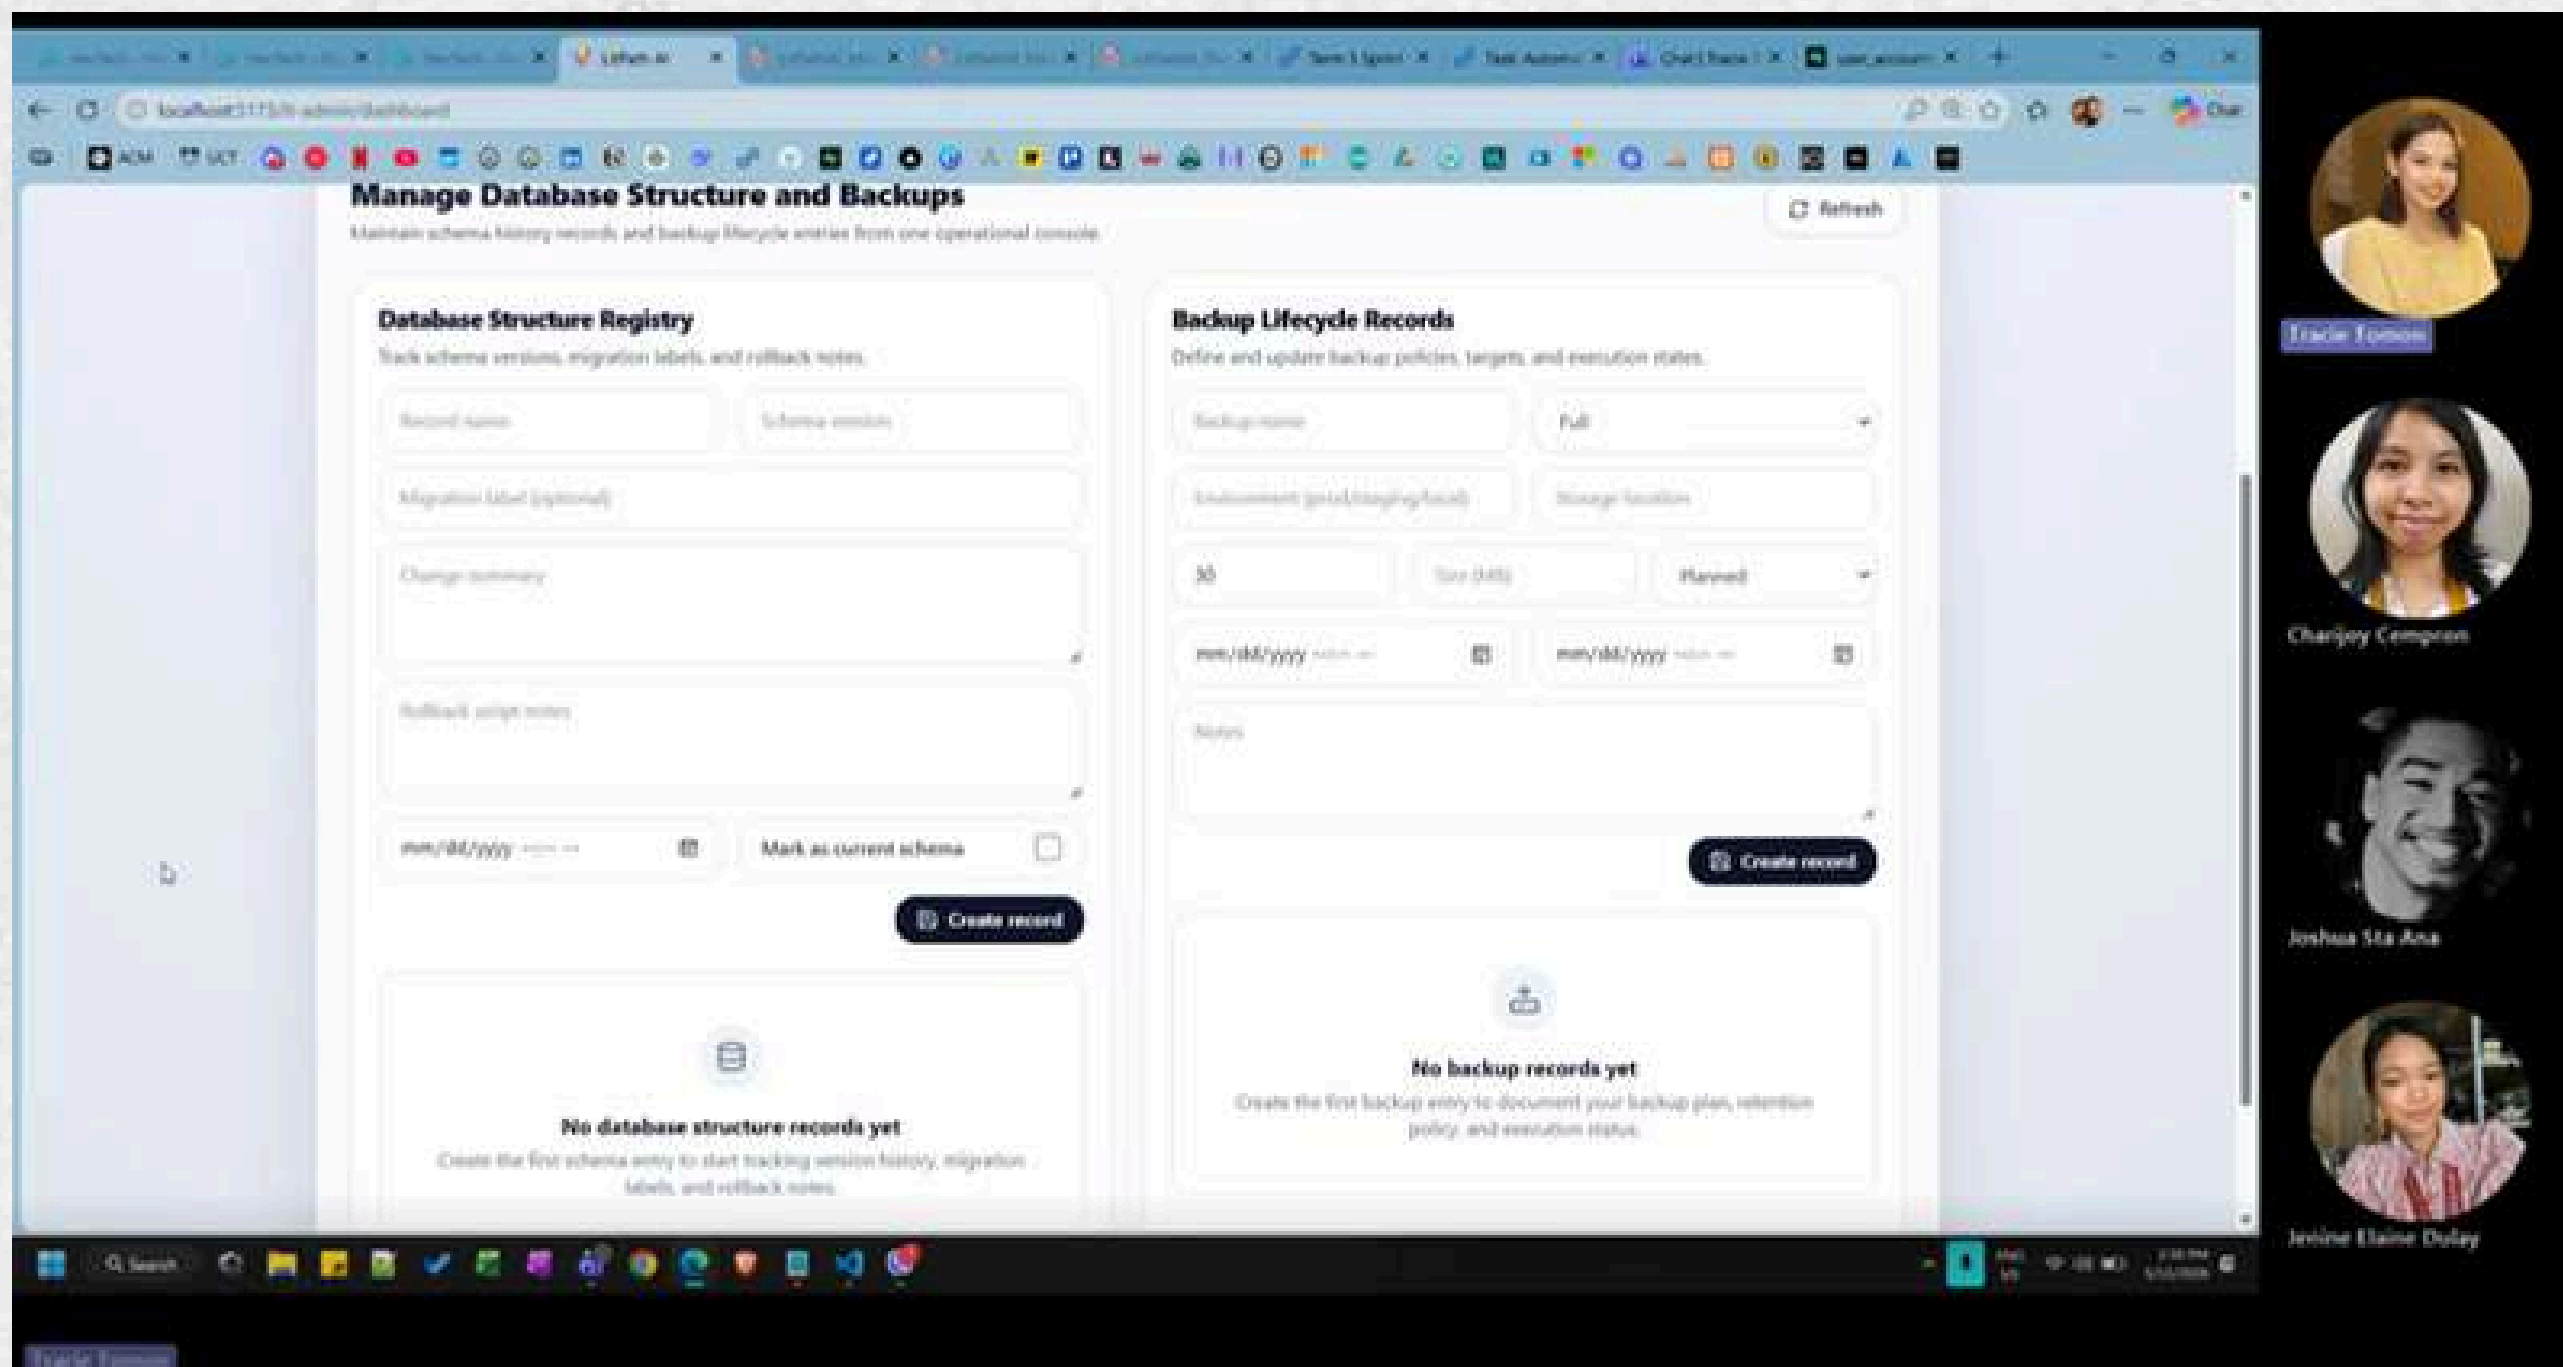

The screenshot shows a web application titled "Manage Database Structure and Backups" with a subtitle "Maintain schema history records and backup lifecycle entries from one operational console." The interface is divided into two main sections:


- Database Structure Registry:** This section allows users to "Track schema versions, migration labels, and rollback notes." It includes input fields for "Record name" and "Schema version", a "Migration label (optional)" field, a "Change summary" text area, and a "Rollback script notes" text area. At the bottom, there is a date selector (set to "mm/dd/yyyy") and a "Mark as current schema" checkbox. A "Create record" button is located at the bottom right of this section.
- Backup Lifecycle Records:** This section allows users to "Define and update backup policies, targets, and execution status." It includes input fields for "Backup name" and "Full" (a dropdown menu), "Execution path (local/remote/cloud)", and "Storage location". It also has fields for "Size" (set to "GB") and "Type" (set to "Full"), and a "Frequency" dropdown menu. Below these are two date selectors (both set to "mm/dd/yyyy") and a "Notes" text area. A "Create record" button is located at the bottom right of this section.

Both sections have a "No records yet" message at the bottom, encouraging users to "Create the first [record/entry] to start tracking [version history/backup plan, retention policy, and execution status]." The application is displayed within a browser window, and the video conference interface on the right shows four participants: Tracie Tomon, Charjoey Compro, Joshua Sta Ana, and Jerline Elaine Dula.



Agile Scrum Ceremonies

Sprint 2 Retrospective meeting

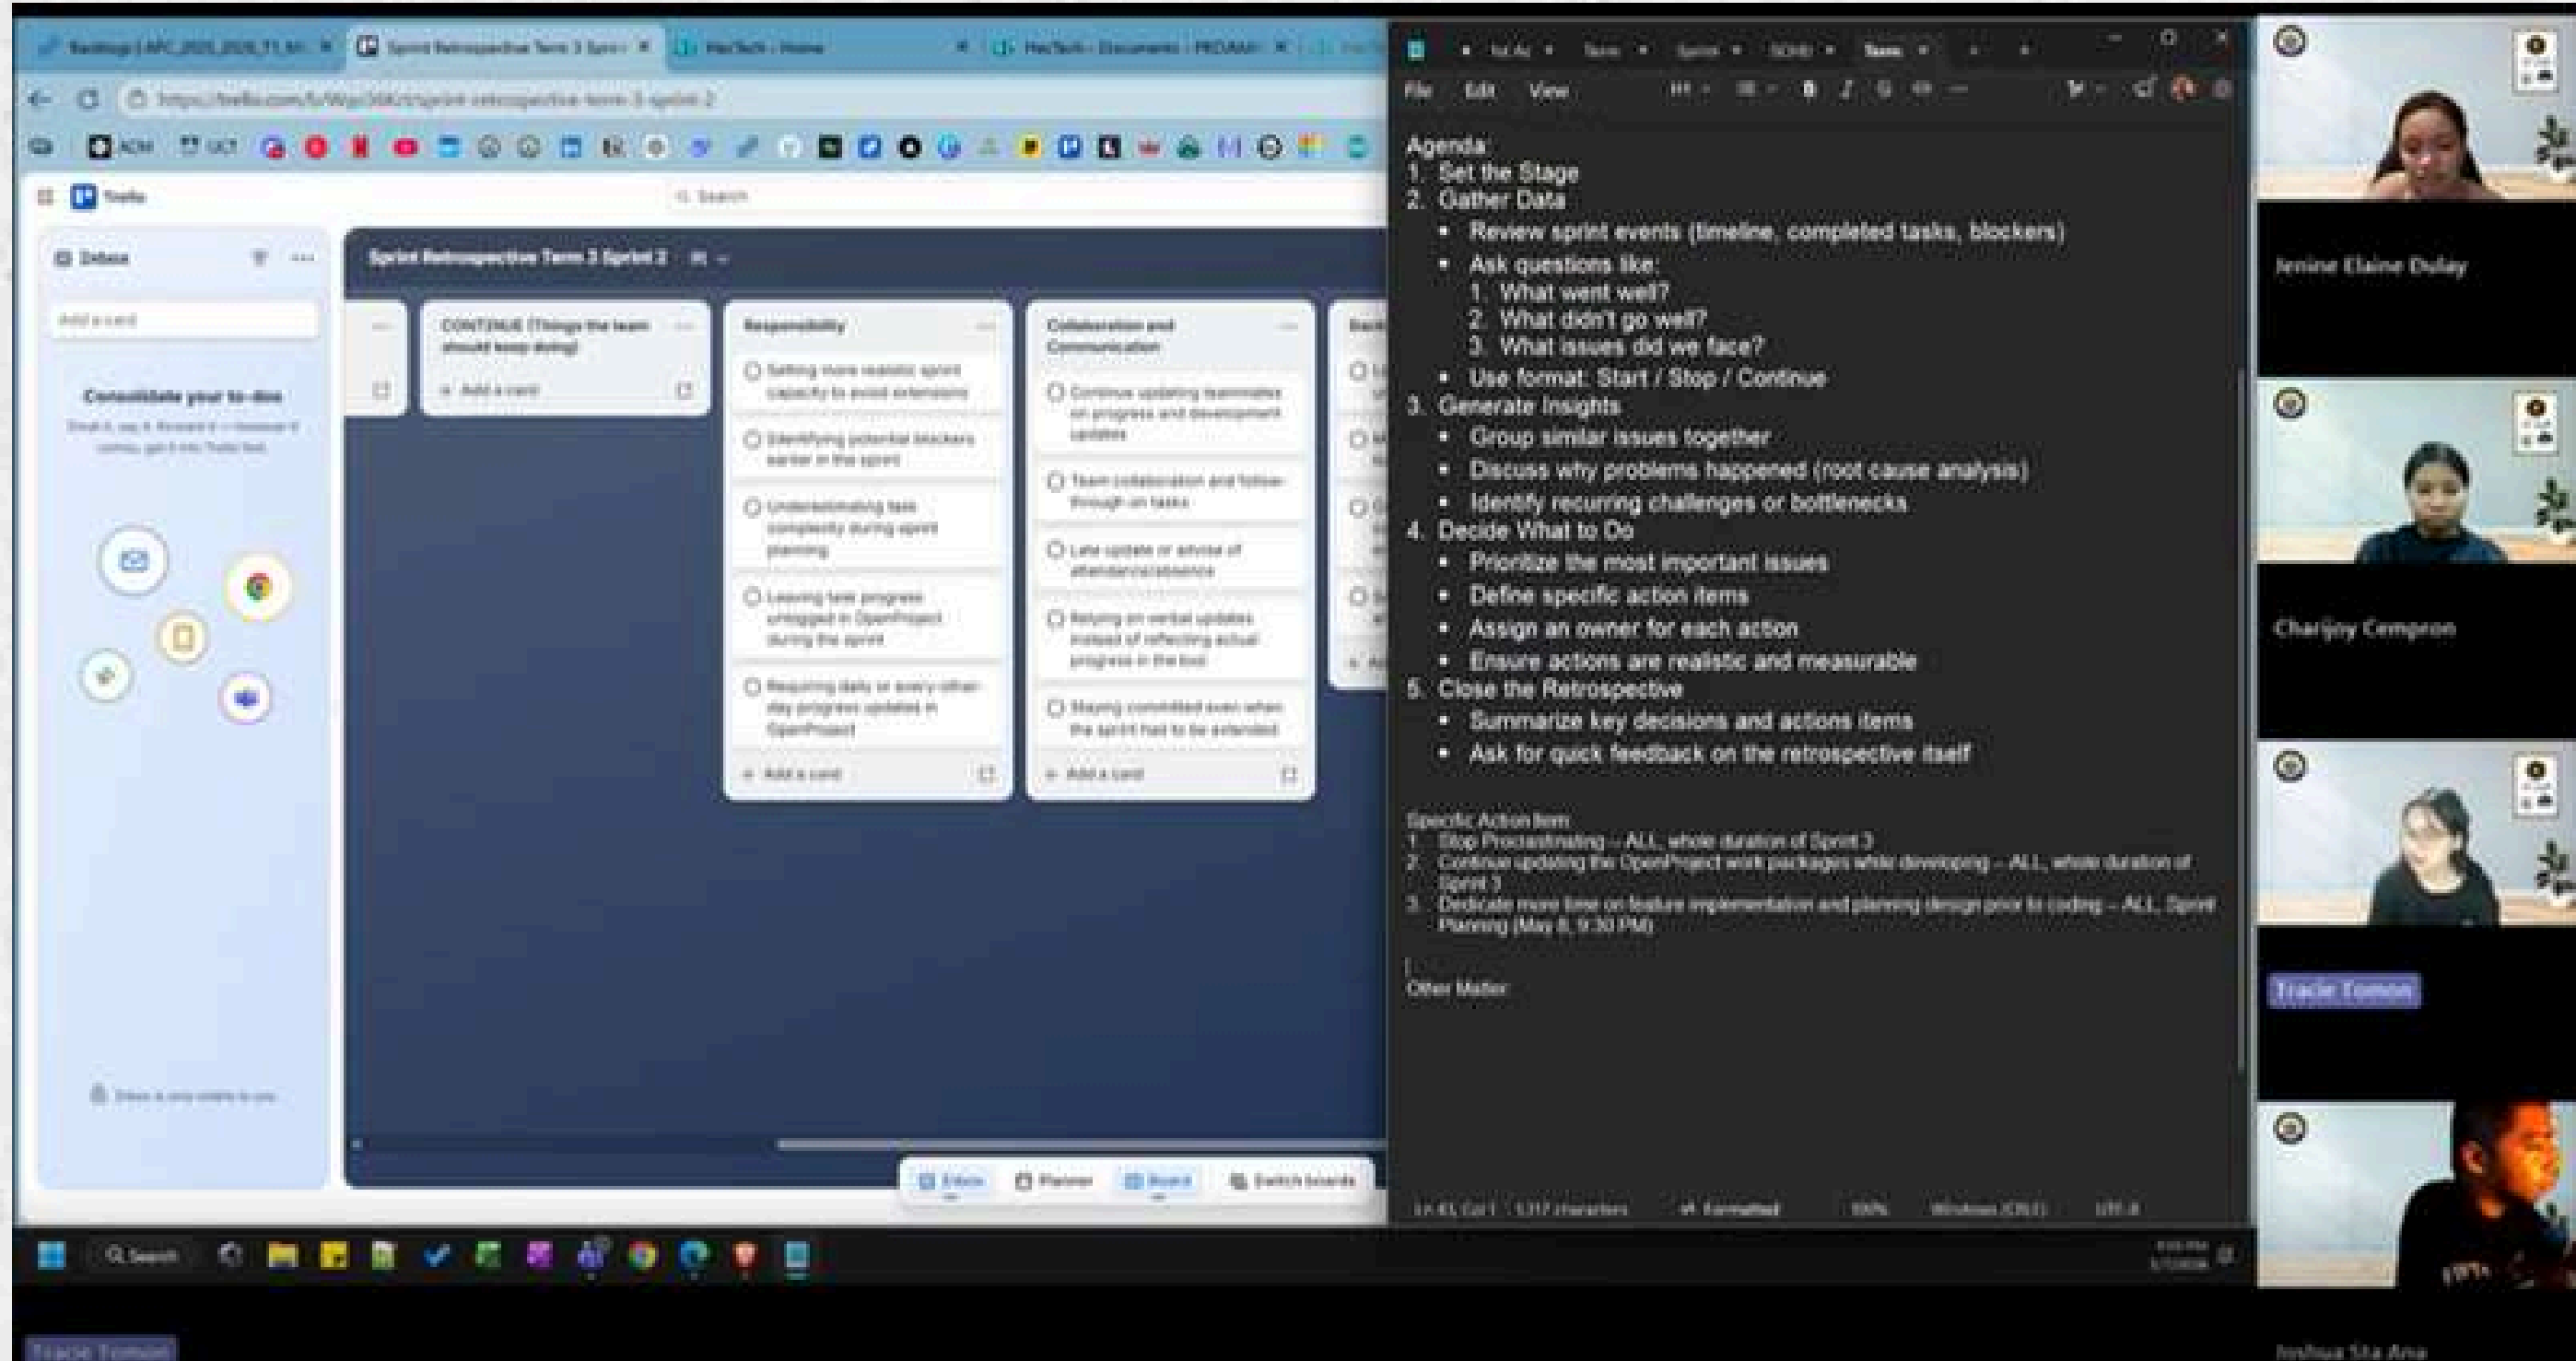

The screenshot displays a Zoom meeting interface. On the left, a Trello board titled "Sprint Retrospective Term 3 Sprint 2" is visible. The board has four columns: "CONTINUE (Things the team should keep doing)", "Responsibility", "Collaboration and Communication", and "Blockers". The "CONTINUE" column contains several cards with tasks like "Setting more realistic sprint capacity to avoid extending", "Identifying potential blockers earlier in the sprint", "Understanding task complexity during sprint planning", "Leaving team progress unlogged in OpenProject during the sprint", and "Resolving daily or every other day progress updates in OpenProject". The "Responsibility" column has cards for "Identifying potential blockers earlier in the sprint", "Understanding task complexity during sprint planning", "Leaving team progress unlogged in OpenProject during the sprint", and "Resolving daily or every other day progress updates in OpenProject". The "Collaboration and Communication" column has cards for "Continuous updating team member on progress and development updates", "Team collaboration and follow-through on tasks", "Late update or arrival of attendance/absence", "Relying on verbal updates instead of reflecting actual progress in the tool", and "Missing committed even when the sprint had to be extended". The "Blockers" column is empty. On the right, a list of agenda items is shown:

- Agenda:
- 1. Set the Stage
- 2. Gather Data
 - Review sprint events (timeline, completed tasks, blockers)
 - Ask questions like:
 - 1. What went well?
 - 2. What didn't go well?
 - 3. What issues did we face?
 - Use format: Start / Stop / Continue
- 3. Generate Insights
 - Group similar issues together
 - Discuss why problems happened (root cause analysis)
 - Identify recurring challenges or bottlenecks
- 4. Decide What to Do
 - Prioritize the most important issues
 - Define specific action items
 - Assign an owner for each action
 - Ensure actions are realistic and measurable
- 5. Close the Retrospective
 - Summarize key decisions and actions items
 - Ask for quick feedback on the retrospective itself

Specific Action Item

- Stop procrastinating – ALL, whole duration of Sprint 3
- Continue updating the OpenProject with packages while developing – ALL, whole duration of Sprint 3
- Dedicate more time on feature implementation and planning design prior to coding – ALL, Sprint Planning (May 8, 9:30 PM)

Other Matter

On the right side of the Zoom window, a vertical stack of participant video feeds is visible. The participants are: Jennine Elaine Dula, Charjey Campeon, Tracie Tomon, and Tomon, Tracie. The Zoom status bar at the bottom shows "14:41 GMT+8 5:17 (Thursday)", "14:41 GMT+8", "100%", "Windows (32-bit)", and "175.8".

Tomon, Tracie




AGILE SCRUM DOCUMENTS




Agile Team Charter

Tools



Communication



Development



Project Tracking



Document Management



Agile Team Charter


Rules of Behavior



Communication
(Attendance, Feedback)



Task Management (Task
Tracking, Documentation)



Project Control (Escalation,
Change Control)



Quality Assurance (Review)



Agile Scrum Documents


Agile Team Values




Initiative




Commitment



Transparency

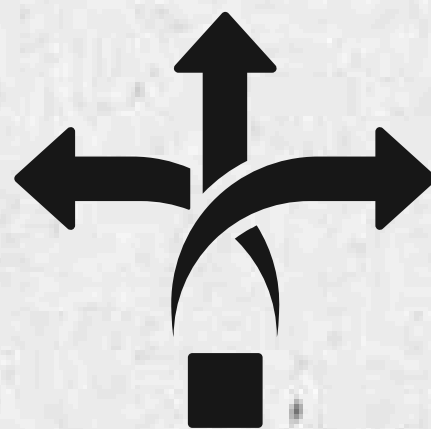

Flexibility

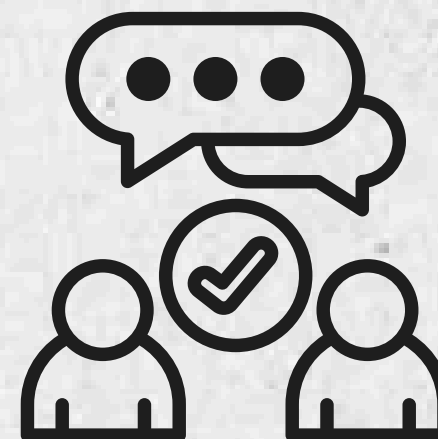

Communication



Accountability



PMBOK

01 INITIATION PHASE



PROJECT CHARTER

Project Scope and Business Need

Project Scope

- AI-powered web app for DOST-STII Library
- Semantic search for theses and dissertations
- Features: summaries, citations, bookmarks, history, admin dashboard
- Covers design, development, testing, and deployment

Business Need

- Current OPAC has limited keyword search and vague results
- Students and library staff need faster, more relevant research outputs
- Solution leverages AI (embeddings & LLMs) for a better search experience



PROJECT CHARTER


Objectives




Improve accuracy
and relevance of
search results



Enhance research
efficiency for
students and staff



Provide faster query
processing and result
display



Enable intelligent
features
(Citations, bookmark,
follow-up queries)



PROJECT CHARTER

Milestone Schedule

LitPath AI: Smart Pathfinder for Theses and Dissertations

April 2025 – July 2026

■ Completed
 ■ In progress
 ■ Not started

Milestone	APR 25	MAY 25	JUN 25	JUL 25	AUG 25	SEP 25	OCT 25	NOV 25	DEC 25	JAN 26	FEB 26	MAR 26	APR 26	MAY 26	JUN 26	JUL 26
Project scoping	Completed															
Information gathering	Completed															
Completion of Project Deliverables & Documentation	Completed	Completed	Completed													
Design thinking (stages 1-5)			Completed	Completed	Completed											
Core UI dev (UI, citations, bookmarks)						Completed	Completed									
AI search, overview, feedback & dashboard							Completed	Completed	Completed	Completed						
Feature refinement											Completed	Completed				
Dev & performance optimization												In progress	In progress	In progress		
Proxmox deployment & internal testing														In progress		
Bug fixes & usability testing														Not started	Not started	
Final deployment															Not started	Not started


Timeline runs Apr 2025 → Jul 2026



PROJECT BRIEF

PROBLEM

- Keyword-only search
- Slow results (>1 min)
- Manual Filtering



SOLUTION

- Understands intent
- Fast results
- Finds relevant papers



Business Case

Cost Benefit Analysis

Action	Action Type	Description
System Development by HecTech	Cost	4-member HecTech team contributing labor across six development phases
Cloud Hosting & Infrastructure	Cost	Hosted on Proxmox server for development
AI / LLM API Integration (Gemini AI)	Cost	Operational costs for RAG and Gemini AI during development and live operation
Reduction in manual research time	Benefit	Semantic search reduces search time
Elimination of manual citation formatting	Benefit	Automated citation generation in APA, MLA, Chicago, and IEEE removes manual formatting
Improved system response time	Benefit	Query response time reduced to fit the industry standard



Stakeholder Analysis

Name	Department / Company	Position	Objectives, Requirements, Interests	Project Contribution	Resistance	Power and Interest
Mr. Napoleon Juanillo, Jr. PhD	DOST-STII	Assistant Secretary for Technology Transfer, Communications and Commercialization and Officer-in-Charge, Office of the Director	Research commercialization and partnership development	Provides projects to be worked on by the students	Concerned about budget allocations	High
Ms. Khasian Romulo	DOST-STII	Science Research Specialist II	Efficient research discovery and modernize search capabilities	Requirements definition, supports work, and approves deliverables	Concerned about changing initial requirements mid-project	High
Mr. Jonathan Abalon	DOST-STII	Science Research Specialist II	Improve user satisfaction and increase research utilization	System access and technical support	Concerned about the problems that might arise during system integration	High
Mr. Sean Sanchez	APC	Project Based Learning Coordinator	Educational innovation and and partnership development	Project sourcing	Concerned about partner organizations modifying project scope	High
Mr. Gonzalo Guumogda	APC	SoCIT Faculty/ Project Adviser	Student academic success and skill development	Project guidance, technical mentorship and approves deliverables	Concerned about timeline delays of the deliverables	High
Mr. Jose Quesada	APC	SOCIT Professor	Student academic success and learning outcomes	Technical mentorship and academic evaluation	Concerned about insufficient time for mentorship due to	Medium
End Users	N/A	End Users	Faster research discovery and friendly search interface	User feedback and system testing	Concerned about the interface change of the system	Medium
HecTech Team	APC	Project Developers	Academic achievement and successful project delivery	System development and client communication	Concerned about technical challenges and time constraints	High

Cempron, Charijoy



Stakeholder Management Strategy

Who are the stakeholders?

- DOST-STII — Asst. Sec. Juanillo, Romulo (POC), Abalon (Alt. POC)
- APC — PBL Coordinator, SoCIT Advisers, Student Developers
- External — End Users (students, researchers, DOST employees)

Power–interest quadrants

Manage closely

- Romulo,
- Abalon (high power + high interest)

Keep satisfied

- Asst. Sec. Juanillo (high power, mid interest)

Keep informed

- PBL Coordinator
- Project Advisers
- Developers
- End Users

How we communicate

- Client (DOST-STII) — via Viber
- Dev team — via Microsoft Teams
- Progress tracking — via OpenProject
- Milestones shared with all stakeholders at each sprint review

How we identified stakeholders

Internal brainstorming by the team, validated by project advisers. A stakeholder is anyone who is affected by, can influence, or has a stake in the project's success.

Why it matters

Early identification helps gain support, reduce resistance, and balance competing interests — keeping LitPath AI on track throughout its lifecycle.



Statement of Work

IN-SCOPE FEATURES

- AI Search Engine
- Web App
- Citation Generator
- Bookmarking
- Admin Dashboard
- Feedback System

OUT OF SCOPE

- No digitization
- No database modification
- No full-text hosting

DELIVERABLES



Working System




Documentation



Deployment ready



Business Model Canvas

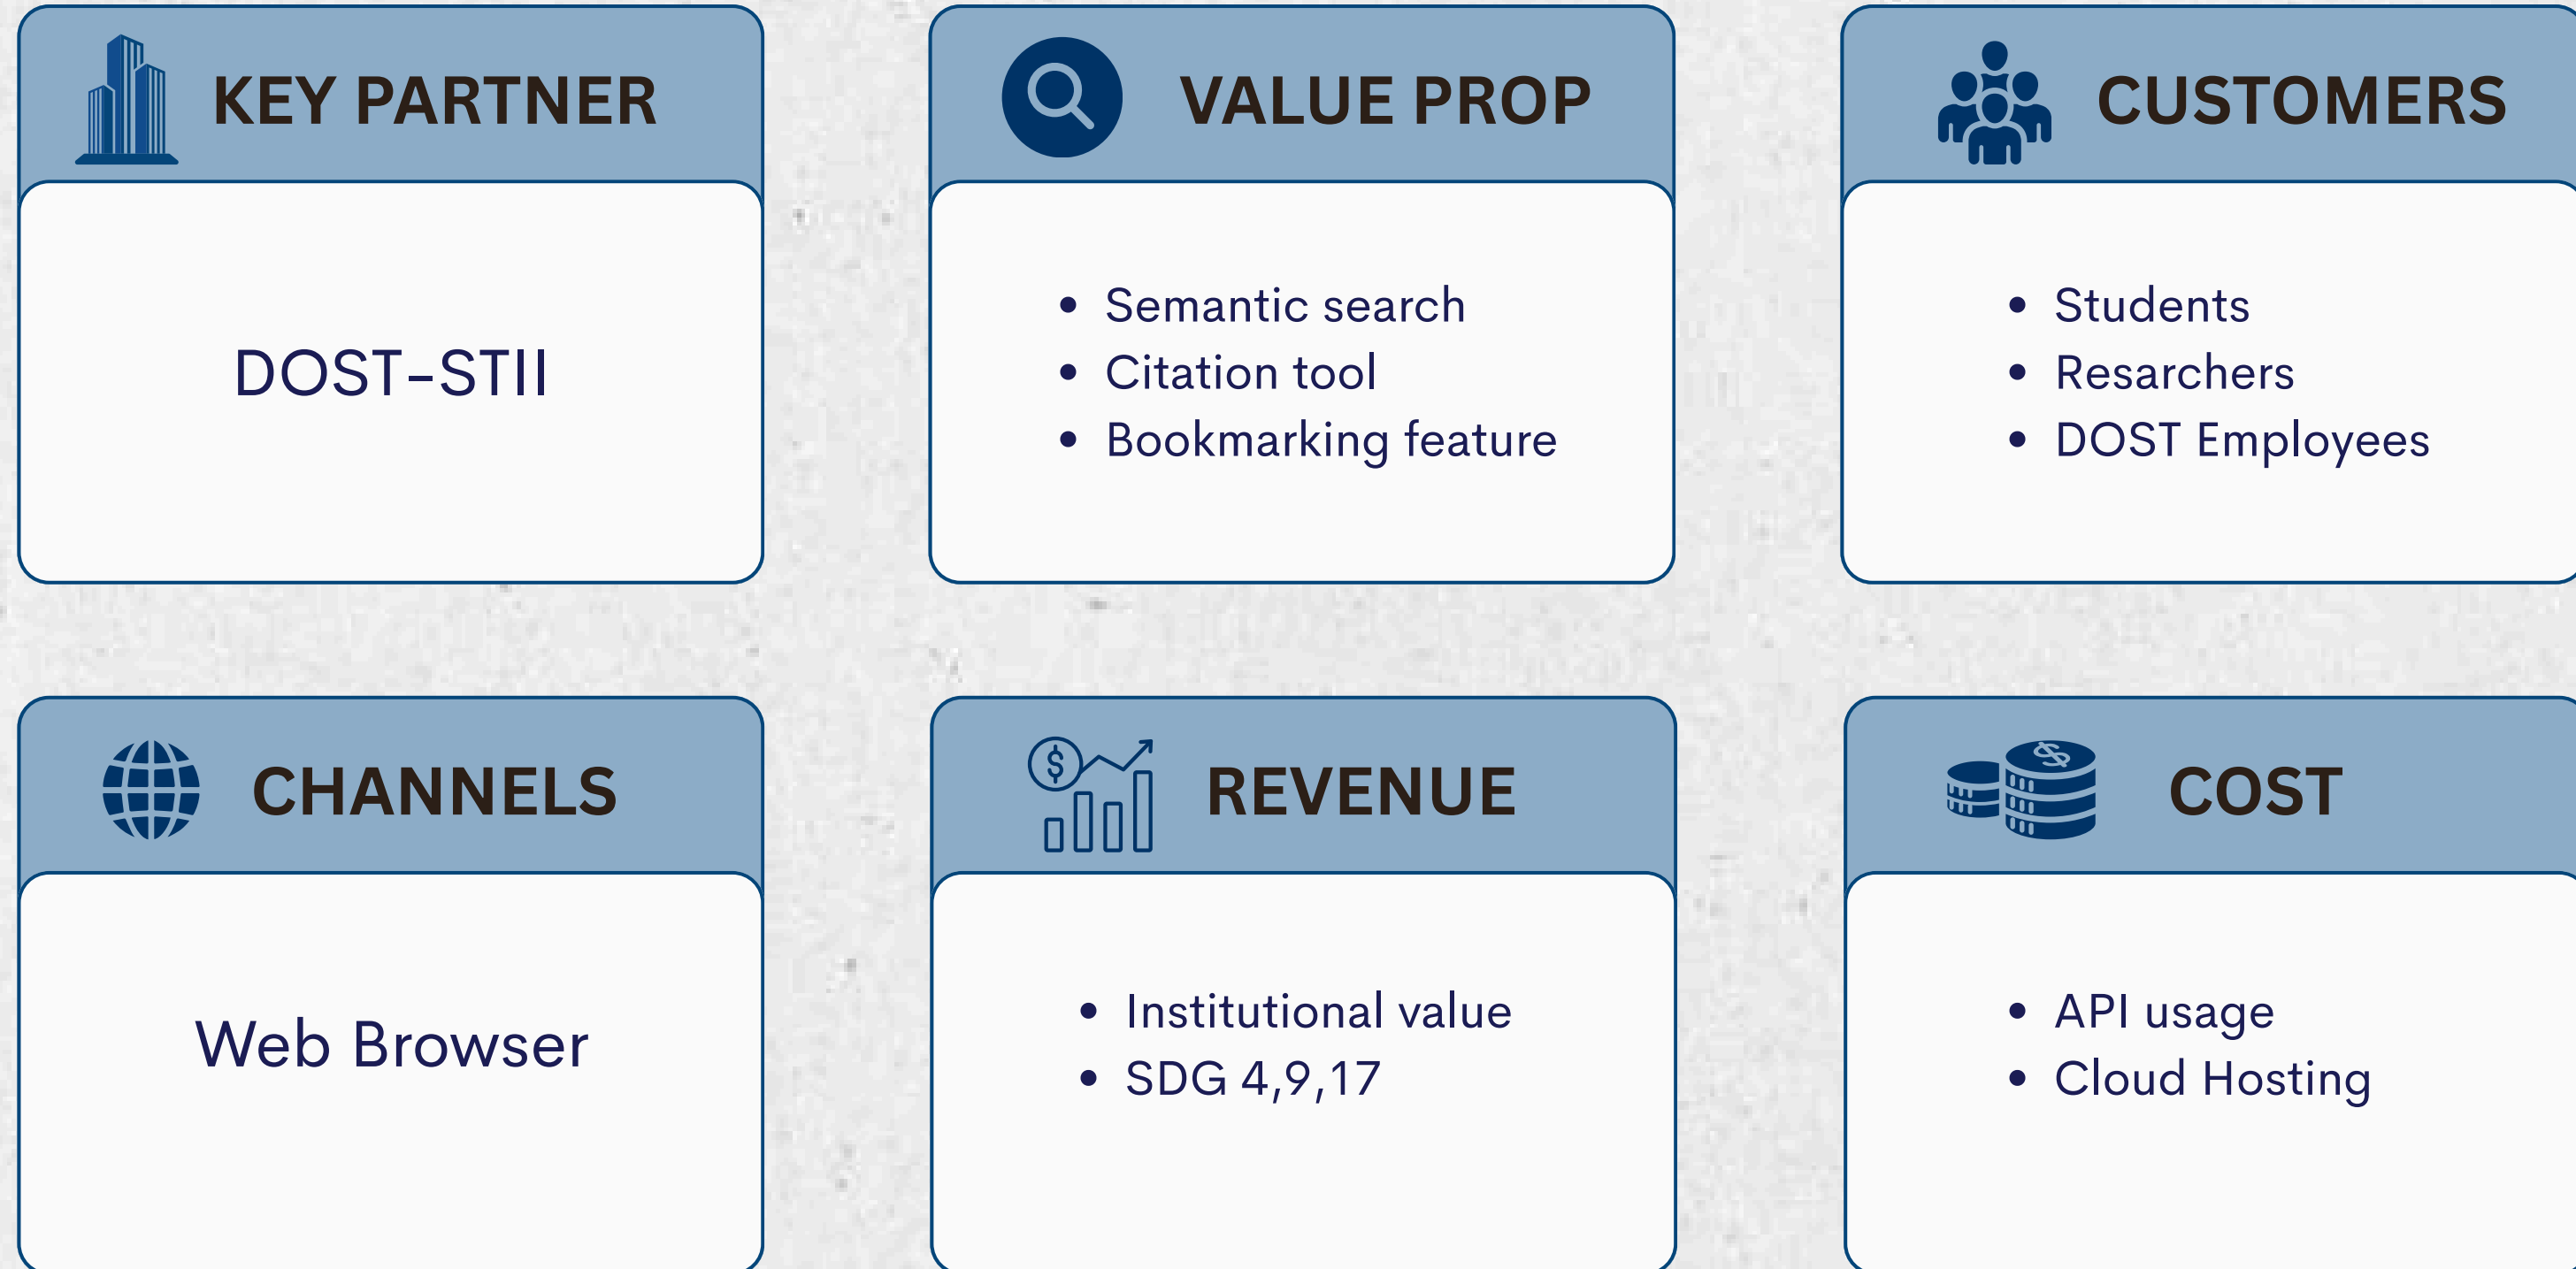

Feasibility Study

PROBLEM

- OPAC uses exact keyword search only
- Queries take over 1 minute
- <70% of results match user intent
- No citation tools or bookmarking

SOLUTION

- RAG-based semantic search (SentenceTransformers + ChromaDB)
- Gemini AI overview summaries
- Citation generator
- Bookmarking, feedback tool, admin dashboard

TARGET USERS

- Students & academic researchers
- DOST employees
- IT Administrator (system management)
- Librarian Administrator (reports & validation)

TECH STACK

React · Django · ChromaDB · Supabase · Gemini 3.0 Flash · Cloudflare · Proxmox (dev)

COST

Development: ₱0 (all open-source).
Post-handover: ₱0–₱2,270/mo (DOST-STII assumes Gemini API + hosting)

SUCCESS CRITERIA

- ≥3.5/5 satisfaction
- ≥70% relevance accuracy
- Results better than the old system
- All deliverables signed off

Recommendation: Proceed with project approval. LitPath AI is technically viable, organizationally ready, and delivers a production-ready AI platform at zero development cost — a strong return on institutional investment for DOST-STII.



PMBOK

02 PLANNING PHASE



Communications Management Plan

Communication Type	Medium	Frequency	Audience	Deliverable	Format
Sprint Planning	Face to face or Microsoft Teams	Once per sprint	Project Team	Sprint Plan, MOTM	Video recording stored on Microsoft Teams channel and SharePoint
Daily Stand-up	Face to face or Microsoft Teams	Daily during active sprints	Project Team	Stand-up MOTM	Video recording stored on Microsoft Teams channel, verbal updates
Backlog Refinement	Face to face or Microsoft Teams	Once per sprint	Project Team	Updated Product Backlog	Video recording stored on Microsoft Teams channel and OpenProject
Sprint Review	Face to face or Microsoft Teams	Once per sprint	Project Team, Project Adviser, Client	Sprint Demo, MOTM	Video recording stored on Microsoft Teams channel and SharePoint



Communications Management Plan

Sprint Retrospective	Face to face or Microsoft Teams	Once per sprint	Project Team	Project Manager	Retrospective MOTM	Video recording stored on Microsoft Teams channel. SharePoint, and Trello Board
Project Status Report	Face to face or Microsoft Teams	Per sprint	Project Sponsor, Project Adviser	Project Manager	Project Status Report	Soft copy sent via Viber
Client Coordination Meeting	Face to face or Microsoft Teams or Viber	As needed	Project Manager, Client	Project Manager	MOTM	Soft copy archived on SharePoint



Scope Management Plan

Collect Requirements

Gather and document requirements through stakeholder interviews, Design Thinking activities, and the Project Charter.

Define Scope

Establish project boundaries, deliverables, constraints, and features based on OPAC limitations and client needs.

Create WBS

Break down project work into manageable packages organized by phases and tracked in OpenProject.

Verify Scope

Review and validate deliverables with the Project Manager and Khasian Eunice Romulo through milestone approvals.

Control Scope

Manage scope changes through formal change requests, impact assessment, and sponsor approval to prevent scope creep.



Work Breakdown Structure

OpenProject Link



Schedule Management Plan

Approach	• Schedule built from WBS deliverables using OpenProject (Gantt charts, task tracking, milestones) • Steps: Activity Definition → Sequencing → Duration Estimating → Resource Assignment • Draft reviewed by full team, then approved by Project Sponsor before baselining
Team Capacity	• 10 hrs/week per member (full-time students, evening sessions) • Rate: ₱500/hour 40 hrs/month per person
Monitoring & Communication	• Bi-weekly schedule reviews via Microsoft Teams • Task updates: actual start/finish dates, % completion, blockers • Tools: Teams (internal) · Viber (client) · OpenProject (official tracking)
Change Threshold	• Changes below 10% variance → Project Manager approves directly • Changes $\geq 10\%$ on a single task or overall timeline → formal change request to Project Sponsor
Scope-Driven Changes	• Scope changes approved by Sponsor may trigger schedule re-baselining • All feature clarifications with DOST-STII must be documented before development begins
Milestones (summary)	✅ Completed: Scoping through Feature Refinement (Apr 2025 – Mar 2026) 🔄 In Progress: Performance Optimization + Proxmox Deployment (Mar – May 2026) 🕒 Upcoming: Bug Fixes, Usability Testing, Final Deployment (May – Jul 2026)



Quality Management Plan: Quality Assurance

- Ensures software quality across SDLC
- Focus on AI accuracy, security, UX, and performance
- Uses QA audits, peer reviews, and CI/CD monitoring
- Applies functional, API, security, and performance testing
- Complies with DOST-STII, OWASP, and DPA 2012 standards
- Final approval through UAT and stakeholder acceptance


KEY METRICS

- $\geq 85\%$ AI accuracy
- $\geq 99.5\%$ uptime
- $\geq 80\%$ test coverage



Human Resource Plan

Resource Calendar

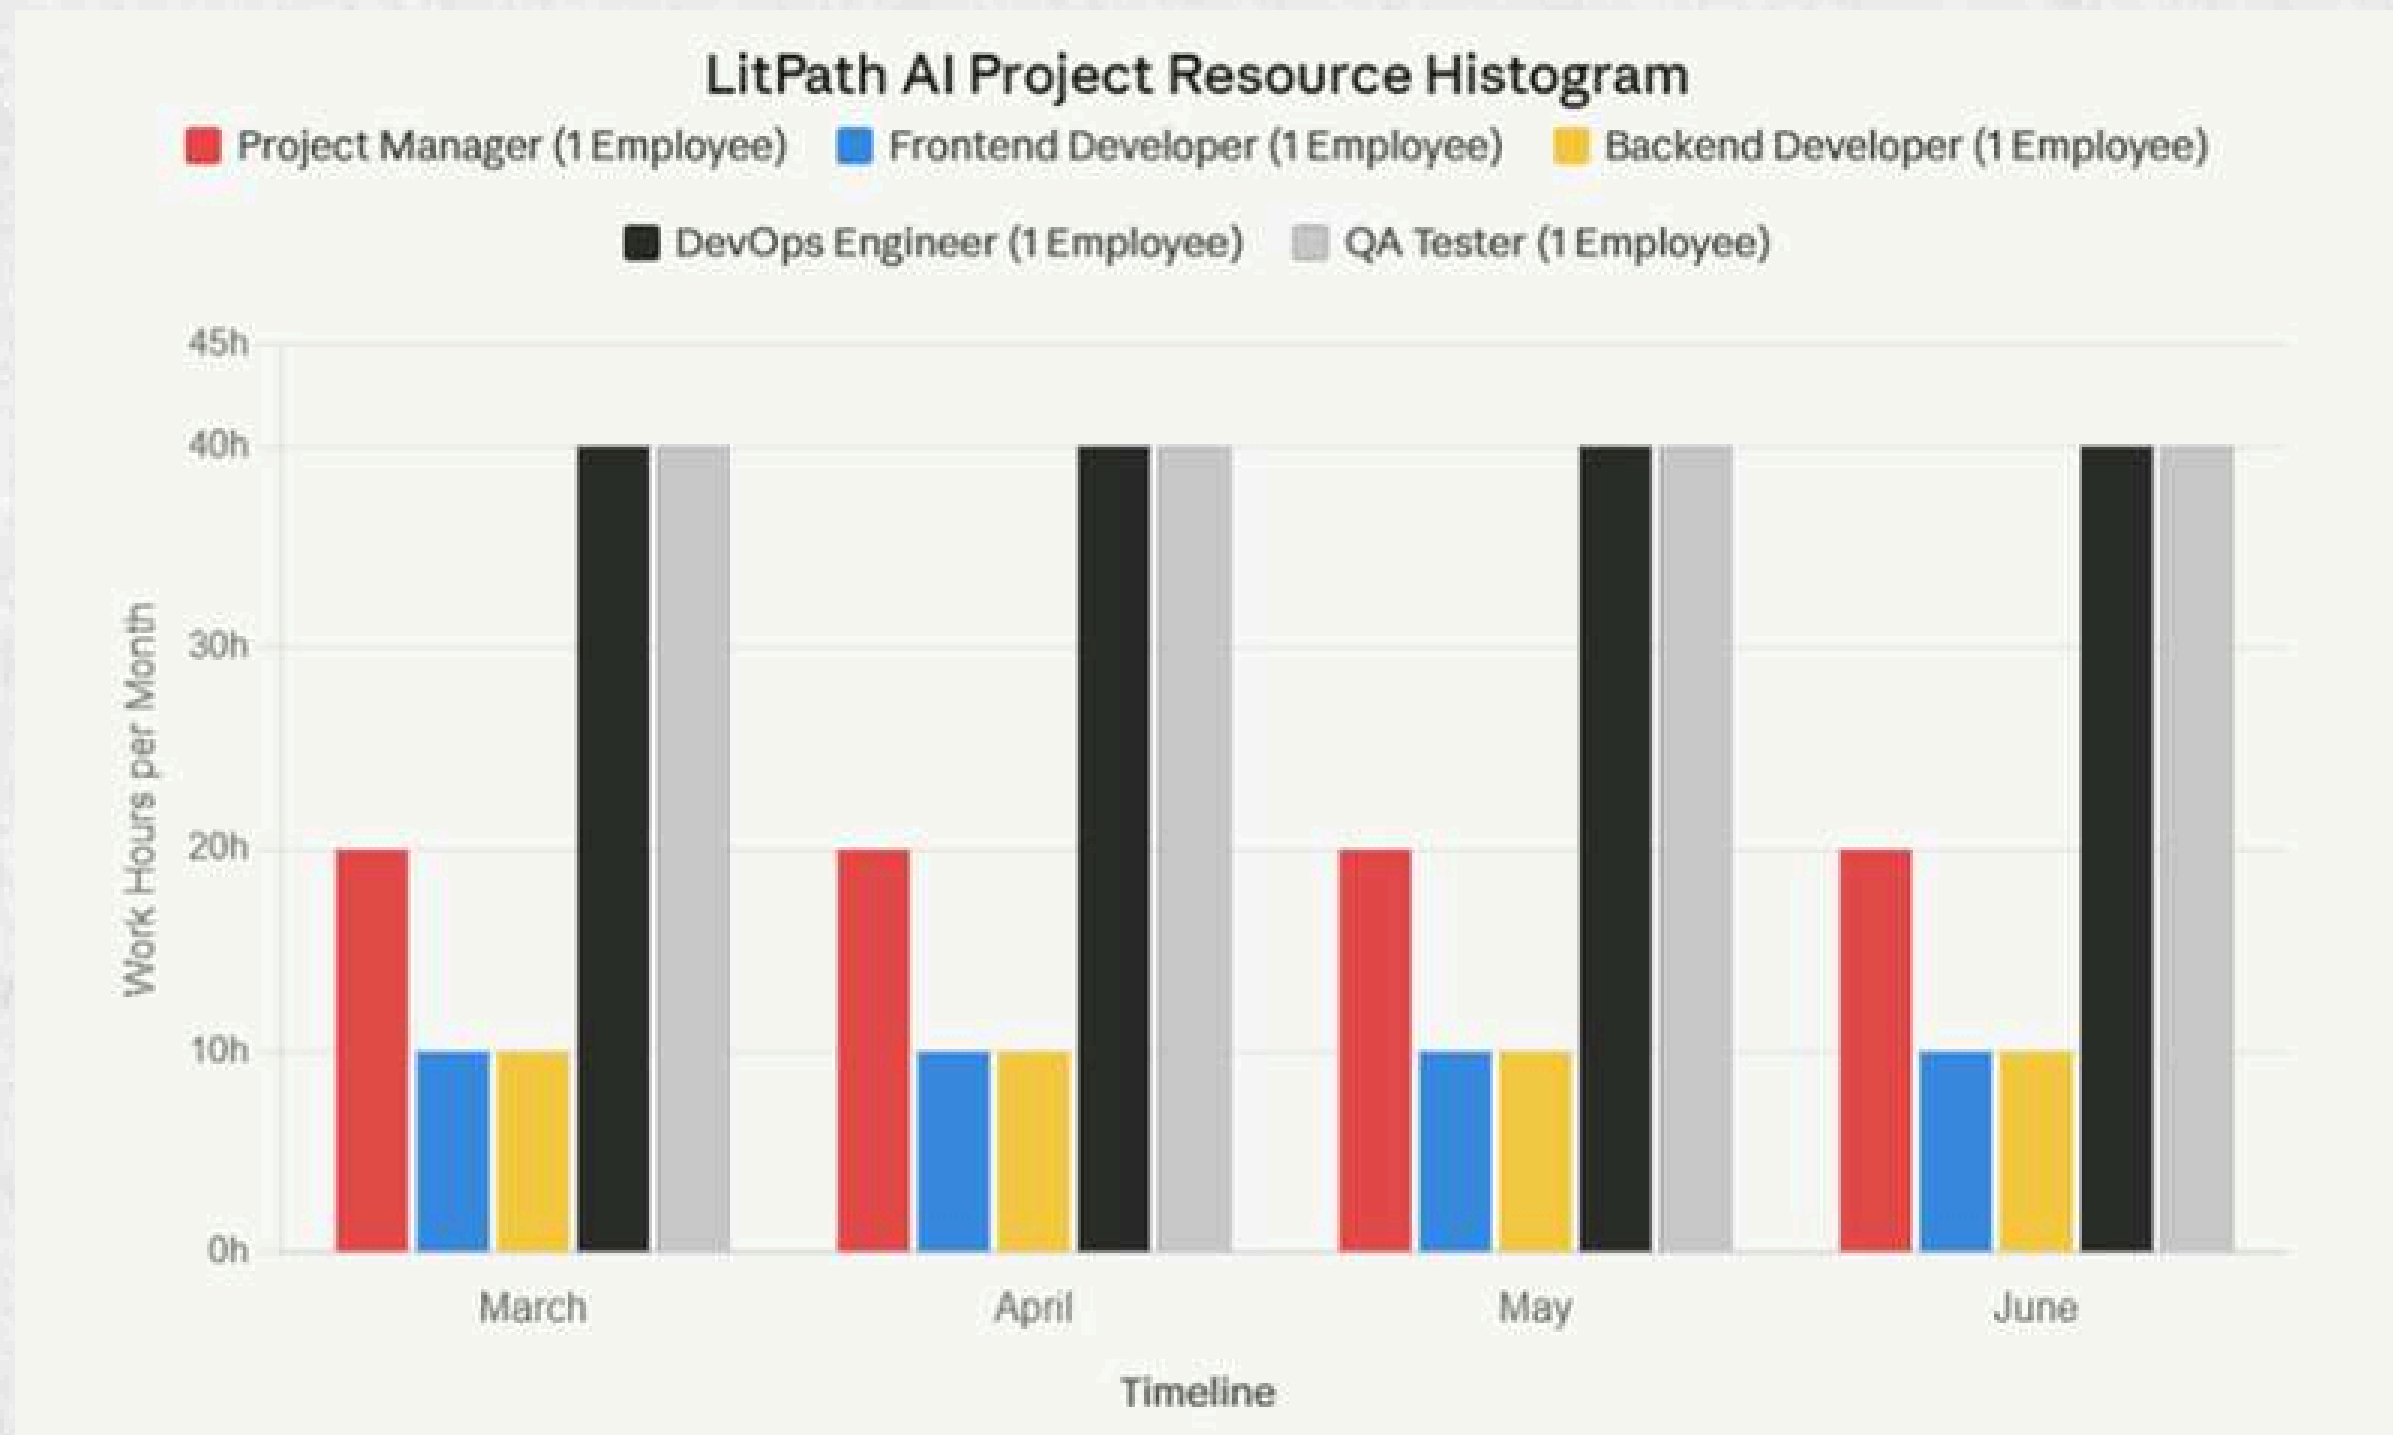

Requirements Management Plan



IDENTIFY

Stakeholder interviews, OPAC gap analysis, benchmarking vs. Google Scholar & Tuklas



PRIORITIZE

High , Medium , and Low scale; core search & integration classified as must-haves



CONTROL CHANGES

Sponsor sign-off required; any change affecting scope, timeline, or database integration must be approved before implementation.



RELEVANCE ACCURACY

70%+



Risk Management Plan

1

GEMINI API UNAVAILABILITY

MITIGATION

Response caching +
fallback vector search

2

LOW SEARCH RELEVANCE

MITIGATION

Iterative RAG pipeline
refinement

3

LLM HALLUCINATION

MITIGATION

Source-grounded
prompting + inline
citations

Monitoring: Bi-weekly sprint reviews via Microsoft Teams and Risk Register updates



Risk Register

Rank	Risk Title	P avg	I avg	Score	Level
1	API Unavailability	4	5	20	Critical
2	Search Relevance Failure	3.25	5	16.25	High
3	LLM Hallucination	3	5	15	High
4	API Latency / Slow Response	3.5	4	14	High
5	Dataset Provision Delay	3.25	4	13	High
6	Cloud Hosting Delay	3	4	12	High
7	Database Inconsistency	2.75	4	11	High
8	Data Loss in Ingestion	3	3.25	9.75	Medium
9	Scope Creep	3	3	9	Medium
10	Data Privacy Non-Compliance	2	4.25	8.5	Medium
11	Dependency / Library Compat.	2.25	3.75	8.44	Medium
12	Key Resource Unavailability	2	4	8	Medium
13	Search Performance Degrad.	2.25	3	6.75	Medium
14	Local Server Hardware Failure	2	3.25	6.5	Medium
15	API Cost Overrun	2	3	6	Medium



Configuration Management Plan

PURPOSE

- Controls system changes and versions
- Ensures stable and consistent system

CHANGE CONTROL

- All changes require CCR approval
- Reviewed by CCB before implementation
- No deployment without approval

CONFIGURATION TRACKING

- CMDB stores versions, files, and changes
- Uses Git for source code control



Change Management Plan

Strategic Approach

Structured vetting process to prevent scope creep and ensure changes align with project objectives. Focused on technical integrity (AI/RAG pipeline) and quality delivery for DOST-STII.

Change Control Board (CCB)

Approval authority meeting during sprint review weeks. Chaired by K. Romulo (Project Sponsor); includes PM, Technical Lead, and System Architect.

7-Step Change Lifecycle

1. Submit
2. Log
3. Evaluate
4. Review
5. Decide
6. Implement
7. Notify

OpenProject
(Tracking)

MS Teams
(Internal)



Viber
(Client Comms)



SYSTEM DESIGN DOCUMENT

System Design Document

Hardware & Software Detailed Design



Hardware: i5 CPU, 32GB RAM, SSD + HDD Storage

Cempron, Charijoy



PMBOK

04 MONITORING AND CONTROLLING PHASE



Project Status Report

WORK COMPLETED

- Search feature implemented
- Other Features implemented (Citation, Bookmark, Search History, Feedback mechanism)
- Cloudflare account setup and repository configuration
- Regression testing improved
- AI model tuning ongoing

OVERALL STATUS

- Progress: ~83% complete
- Phase: Final testing and deployment prep

HEALTH SUMMARY

- Scope: ● On track
- Schedule: ● Slight delay (AI tuning)
- Cost: ● On budget
- Risks: ● AI performance & dataset validation
- Quality: ● High

CURRENT WORK

- AI optimization
- Dataset validation
- UAT preparation
- CCR review & updates




PMBOK

05 CLOSING PHASE



Transition Out Plan

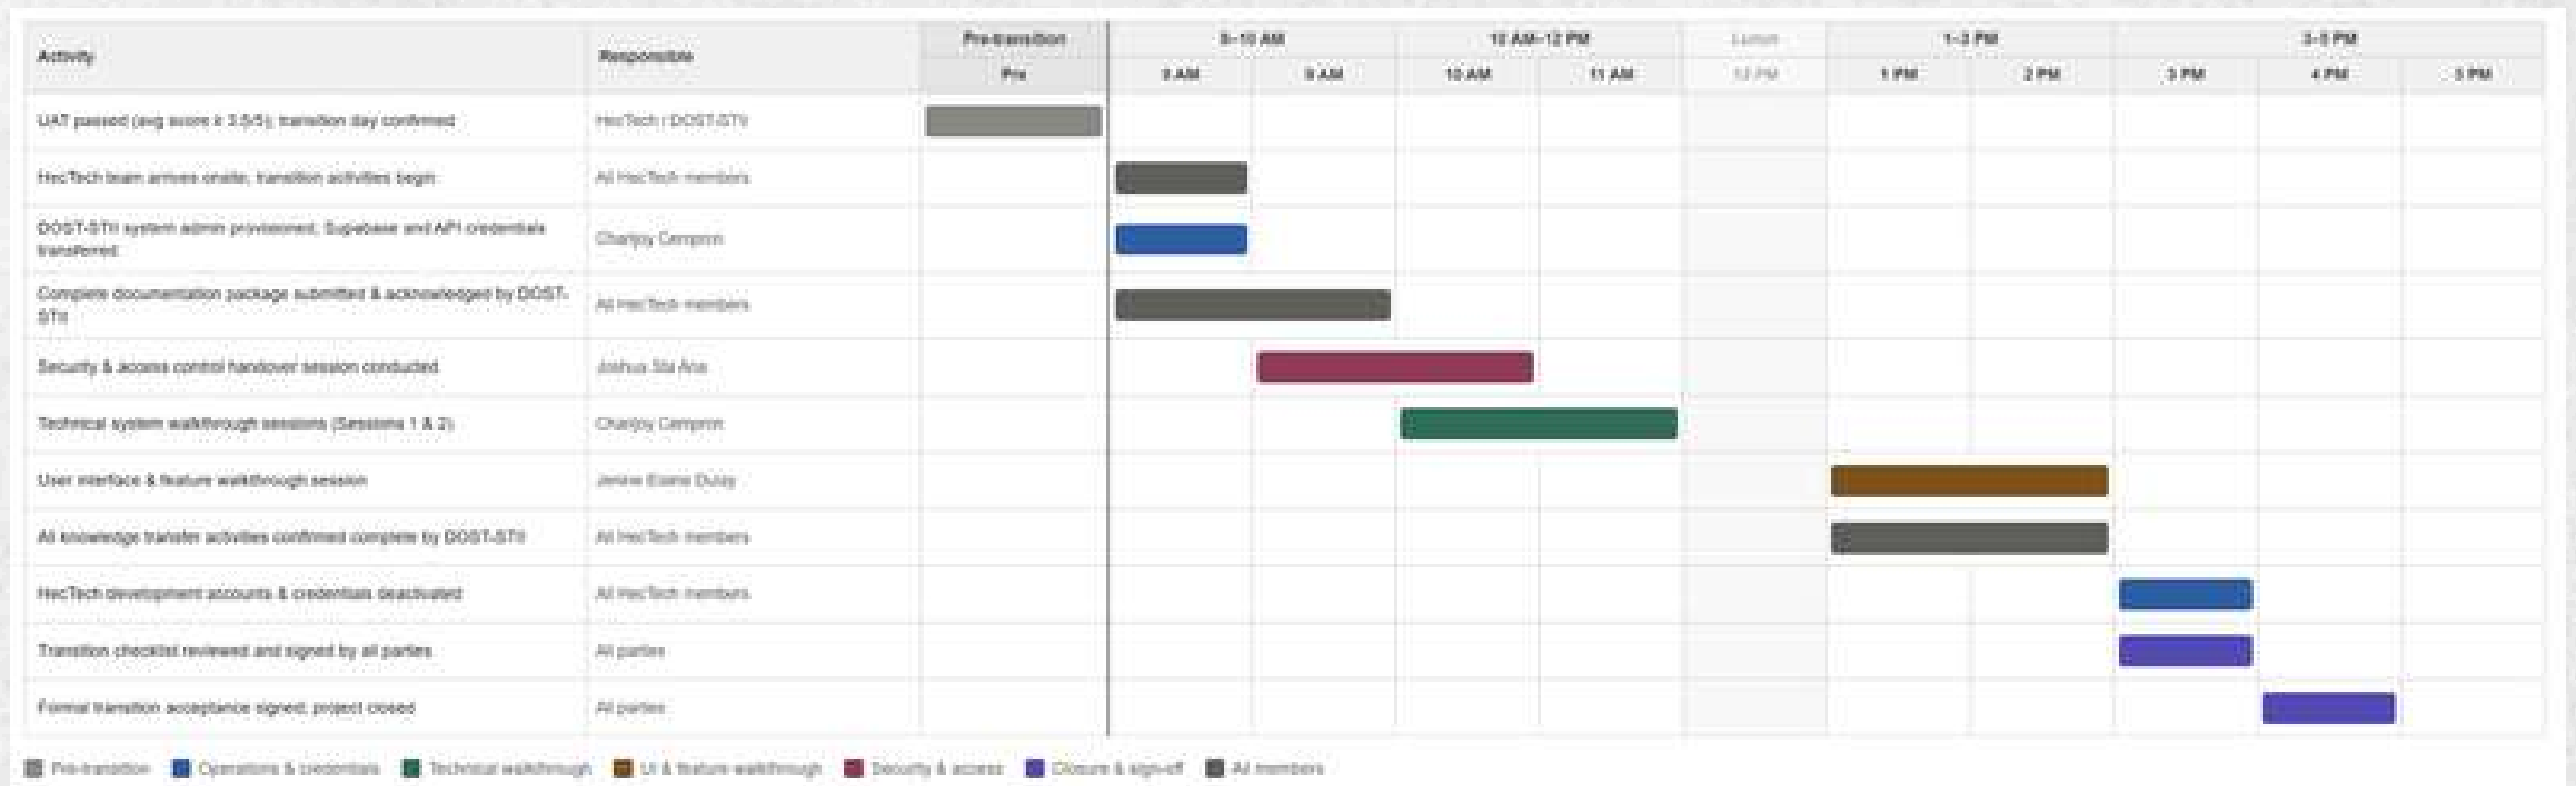

Project Acceptance

Deliverables

1. Working Prototype — RAG-powered semantic search, citation generator (APA/MLA/Chicago/IEEE), bookmarking, feedback tool, admin dashboard
2. Project Documentation — Technical manual, user guide, final report

Acceptance Criteria

1. Working application with all features operational
2. $\geq 3.5/5$ user satisfaction score from testers
3. Deployed via Proxmox, faster results than current OPAC
4. All deliverables formally signed off by stakeholders

Transition to operations

1. Full source code on GitHub with technical reference package
2. Stack: Django · React · Supabase · ChromaDB · Gemini AI
3. Seeding scripts & migration files included for environment setup
4. Gemini API + hosting post-handover

Closeout Activities

1. Post-project review
2. Lessons learned documented & archived
3. HecTech team formally released
4. All PM documents archived for DOST-STII

Sign-off Parties

1. Project Sponsor · DOST-STII
2. Project Manager · HecTech
3. PBL Coordinator · APC
4. Project Adviser · APC



Post-Project Review

DELIVERABLES



Semantic Search (ChromaDB + RAG)



AI Overview Summaries (Gemini AI)



Citation Generator (APA, MLA, Chicago, IEEE,)



Bookmarks & Search History



User Feedback Mechanism



Admin Dashboard



Post-Project Review



PHP 0
Total Dev Cost



Lessons Learned

Lessons from this Project

- Limited document scope — theses & dissertations only; local journals excluded
- No error logging before deployment — Sentry not configured pre-launch

Process improvements

- Feature freeze before deployment
- Wireframe admin features with client early
- ~20% sprint capacity for tech debt
- Formalize CCB from Day 1

How captured

Sprint retrospectives ·
Standups · Group journal

Where stored

OpenProject · SharePoint

Prior references

- Agile curriculum
- RAG best practices
- API risk guidelines

Tomon, Tracie



COSTS

Tomon, Tracie



Planned Value (PV)

₱90,700

Actual Cost (AC)

₱13,323.50

CPI

6.81

SPI

1.00

Sprint budget at a glance

Labor (4 members × 20 hrs × ₱500)	₱40,000
Co-working space (80 hrs × ₱100)	₱8,000
Contingency Reserve (4 × ₱10,000)	₱40,000
Internet + Cloud	₱1,100
Food + Transport	₱1,600
Total PV	₱90,700

- Note on CPI 6.81: High CPI due to incomplete hour logging in OpenProject — not all effort was recorded per task. Team commits to real-time logging in Sprint 2.



OPENPROJECT

Cempron, Charijoy



Roadmap

1.12 AY 2025-2026 T3 Sprint 02

Start date 04/22/2026

Finish date 05/09/2026

Version for Term 3 Sprint 02

100% Total progress

29 closed (100%) 0 open (0%)

Related work packages ^

- ~~Task #6391~~: Re-create sprint in the OpenProject to sync with the burndown
- ~~Task #6392~~: Use OpenProject to update work package status to In Progress first before closing and track progress
- ~~Task #6639~~: Implement an activity logging system that records the user ID, action performed (e.g., review, validate, edit), timestamp, and affected feedback entry when
- ~~Task #6641~~: Design and implement a role-based access control (RBAC) system for IT Administrator and Librarian Administrator, with configurable permissions such as
- ~~Task #6703~~: Export Dormant Materials Only from Material Rating Tab
- ~~Task #6705~~: Set 1-Month Inactivity Rule for Dormant Material Classification
- ~~Task #6706~~: Display Upload Date on Materials to Distinguish Dormant from Recently Uploaded
- ~~Task #6707~~: Add Dedicated Detail Page per Material Rating Metric with Expanded Content on Click
- ~~Task #6708~~: Restructure Dashboard Navigation to Nest Thesis Usage Overview and Material Ratings Under a Single Dashboard Menu
- ~~Task #6790~~: Add Status dropdown filter component alongside Category
- ~~Task #6799~~: Add Category dropdown filter component to the feedback/report list screen
- ~~Task #6802~~: Create CSV export endpoint that applies active filter params before generating output
- ~~Task #6899~~: Implement User Session Duration Logging
- ~~Task #6900~~: Automatically Record Upload Date for Materials
- ~~Feature #6514~~: Feature 14.0 Query Duration Logging & "Upload Date" Tracking
- ~~Feature #6515~~: Feature 15.0 Feedback Filtering Realignment & Advanced Report Filtering
- ~~Feature #6516~~: Feature 16.0 CSV Export Enhancement and PDF Report Export
- ~~Feature #6524~~: Feature 17.0 Admin Hierarchy
- ~~Feature #6525~~: Feature 18.0 Add monitoring on who edited for tracing and logs user id and actions
- ~~Feature #6526~~: Feature 12.0 Targeted Dormant Material Export
- ~~Feature #6527~~: Feature 13.0 Least Viewed Metric tracking
- ~~User story #6638~~: As a Librarian Administrator, I want to track and log who reviews and validates user feedback (including user ID and actions taken) so that we can en
- ~~User story #6640~~: As an IT Administrator, I want to define and manage a hierarchy of admin roles (IT Administrator and Librarian Administrator) with specific permisso
- ~~User story #6702~~: As a Librarian Administrator, I want to export a targeted list of dormant materials (not accessed for 1 month) from the LitPath AI dashboard, so that I
- ~~User story #6704~~: As a Librarian Administrator, I want to view a Least Viewed Materials metric in the Material Rating tab replacing the Top Least Accessed metric, so th
- ~~User story #6796~~: As a Librarian Administrator, I want to filter feedback records by Category and Status. So that I can quickly isolate specific subsets of feedback data a
- ~~User story #6801~~: As a Library Administrator, I want to export feedback data to CSV or PDF based on the filters I've applied, so the file only includes the specific data I
- ~~User story #6804~~: As an admin, I want the system to automatically log how long each user stays in a session so that I can monitor user engagement and activity.
- ~~User story #6805~~: As an admin, I want the upload date of each material to be automatically recorded so that I can track when it was added to the system.

Cempron, Charijoy




Work Packages

ID	SUBJECT	TYPE	STATUS	ASSIGNEE	PRIORITY	PROJECT PHASE	VERSION
625	3.0 Securing Phase	PHASE	In progress	Charijoy Cempron	Normal	Executing	0.10 alpha
6261	Re-create sprint in the OpenProject to sync with the burndown	TASK	Closed	Trace Tironon	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6262	Use OpenProject to update work package status to In Progress first before closing and track progress	TASK	Closed	Trace Tironon	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6214	Feature 14.0 Query Duration logging & "Upload Date" tracking	FEATURE	Closed	Archie Sta Ana	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6213	Feature 15.0 Feedback Filtering Reassignment & Advanced Report Filtering	FEATURE	Closed	Jenine Elaine Duly	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6216	Feature 16.0 CSV Export Enhancement and PDF Report Export	FEATURE	Closed	Jenine Elaine Duly	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6224	Feature 17.0 Admin Hierarchy	FEATURE	Closed	Charijoy Cempron	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6640	As an IT Administrator, I want to define and manage a hierarchy of admin roles (IT Administrator and Librarian Administrator) with specific permissions.	USER STORY	Closed	Charijoy Cempron	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6641	Design and implement a role-based access control (RBAC) system for IT Administrator and Librarian Administrator, with configurable permissions.	TASK	Closed	Charijoy Cempron	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6225	Feature 18.0 Add monitoring on who edited for tracing and logs user id and actions	FEATURE	Closed	Charijoy Cempron	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6638	As a Librarian Administrator, I want to track and log who reviews and validates user feedback (including user ID and actions taken) so that we can an...	USER STORY	Closed	Charijoy Cempron	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6639	Implement an activity logging system that records the user ID, action performed (e.g., review, validate, edit), timestamp, and affected feedback e...	TASK	Closed	Charijoy Cempron	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6126	Feature 12.0 Targeted Dormant Material Export	FEATURE	Closed	Trace Tironon	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6702	As a Librarian Administrator, I want to export a targeted list of dormant materials (not accessed for 1 month) from the LiPath AI dashboard, so that ...	USER STORY	Closed	Trace Tironon	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6703	Export Dormant Materials Only from Material Rating tab	TASK	Closed	Trace Tironon	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6127	Feature 13.0 Least Viewed Metric tracking	FEATURE	Closed	Trace Tironon	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6704	As a Librarian Administrator, I want to view a Least Viewed Materials metric in the Material Rating tab replacing the Top Least Accessed metric, so th...	USER STORY	Closed	Trace Tironon	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6705	Set 3-MONTH inactivity Rule for Dormant Material Classification	TASK	Closed	Trace Tironon	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6706	Display Upload Date on Materials to Distinguish Dormant from Recently Uploaded	TASK	Closed	Trace Tironon	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6707	Add Dedicated Detail Page per Material Rating Metric with Expanded Content on Click	TASK	Closed	Trace Tironon	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6708	Restructure Dashboard Navigation to Nest These Usage Overview and Material Rating Under a Single Dashboard Menu	TASK	Closed	Trace Tironon	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6213	Feature 15.0 Feedback Filtering Reassignment & Advanced Report Filtering	FEATURE	Closed	Jenine Elaine Duly	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6798	As a Librarian Administrator, I want to filter feedback records by Category and Status, so that I can quickly isolate specific subsets of feedback data an...	USER STORY	Closed	Jenine Elaine Duly	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6798	Add Status dropdown filter component alongside Category	TASK	Closed	Jenine Elaine Duly	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6796	Add Category dropdown filter component to the feedback/report list screen	TASK	Closed	Jenine Elaine Duly	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6216	Feature 16.0 CSV Export Enhancement and PDF Report Export	FEATURE	Closed	Jenine Elaine Duly	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6807	As a Librarian Administrator, I want to export feedback data to CSV or PDF based on the filters I've applied, so the file only includes the specific data I ne...	USER STORY	Closed	Jenine Elaine Duly	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6802	Create CSV export endpoint that applies active filter params before generating output	TASK	Closed	Jenine Elaine Duly	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6514	Feature 14.0 Query Duration logging & "Upload Date" tracking	FEATURE	Closed	Archie Sta Ana	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6804	As an admin, I want the system to automatically log how long each user stays in a session so that I can monitor user engagement and activity.	USER STORY	Closed	Archie Sta Ana	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6808	Implement User Session Duration Logging	TASK	Closed	Archie Sta Ana	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6803	As an admin, I want the upload date of each material to be automatically recorded so that I can track when it was added to the system.	USER STORY	Closed	Archie Sta Ana	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02
6900	Automatically Record Upload Date for Materials	TASK	Closed	Archie Sta Ana	Normal	Executing	1.12 Apr 2025-2026 T3 Sprint 02

Cempron, Charijoy



Gantt Chart

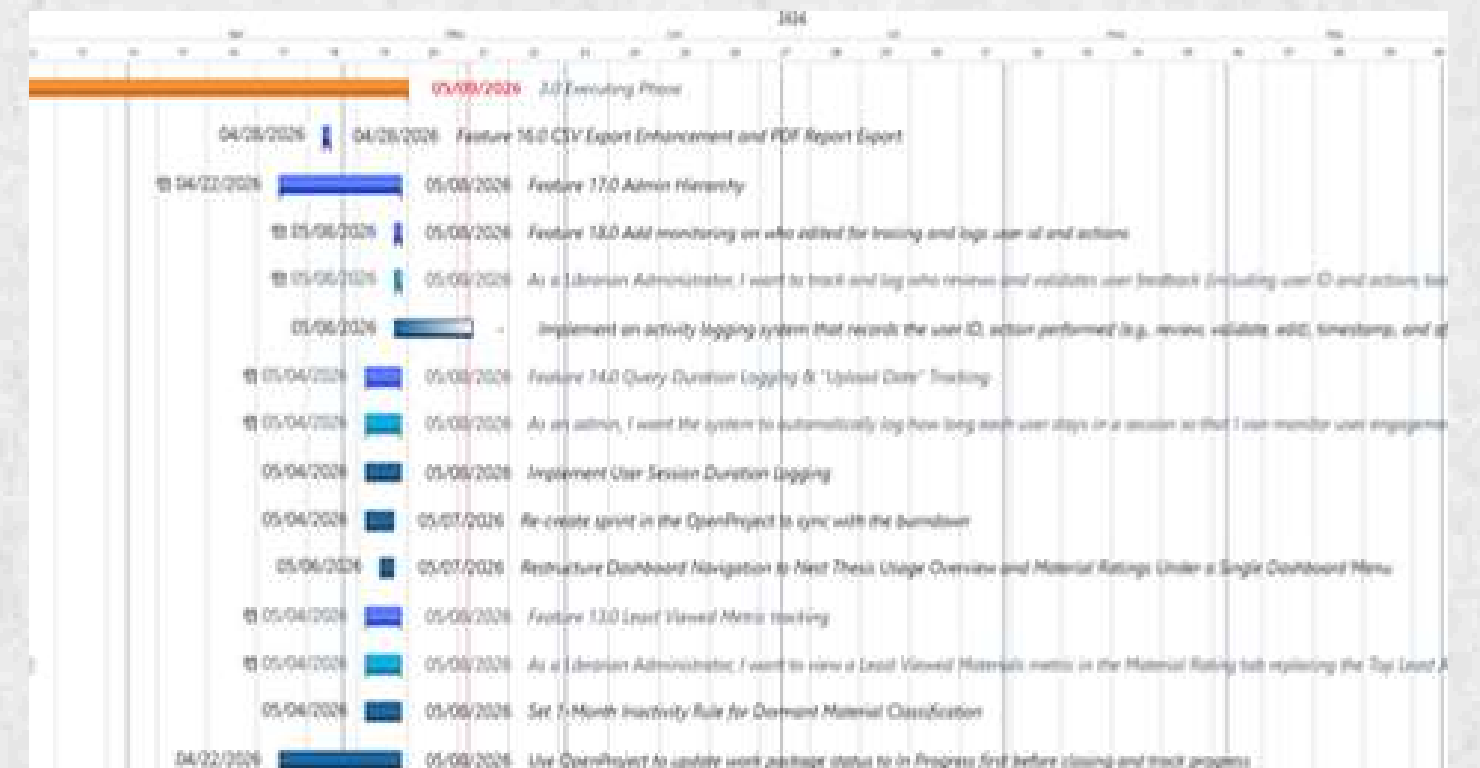

Budgets and Costs

Planned Unit Costs and Planned Labor Costs

OpenProject

Search in OpenProject

APC_2025_2026_T1_M03L...

APC_2025_2026_T1_M03L... / Budgets / Budget #154

Update Copy Delete

Budget #154

Term 3 Sprint 02 Budget

Added by Tania Toman 18 days ago

BUDGET DETAILS

Cost type

Budget

Fixed date

05/06/2026

Spent (ratio)

10%

Description

TOTALS

Base amount

PHP 0.00

Planned unit costs

PHP 50,700.00

Planned labor costs

PHP 40,000.00

Planned

PHP 90,700.00

Spent

PHP 10,700.00

Available

PHP 74,000.00

UNITS

Planned unit costs

UNITS	COST TYPE	COMMENT	BUDGET
80.00	Co-working space (Hourly)	Match with spent time --> Freezone deployment & te...	PHP 8,000.00
1.00	Internet Monthly Subscription Php 1K	Monthly internet for team	PHP 1,000.00
4.00	Contingency Reserve	Sprint 02 contingency	PHP 40,000.00
8.00	Food Allowance	2 meetings x 4 members	PHP 800.00
8.00	Transportation expenses Php 100	2 meetings x 4 members	PHP 800.00
1.00	Cloud Services Monthly Subscription	Cloudflare / Gemini API free tier	PHP 100.00
			PHP 50,700.00

Actual unit costs

WORK PACKAGE	UNITS	COST TYPE	COSTS
task #10101 Re-create sprint in the OpenProject to sync act...	1.50	Co-working space (Hourly)	PHP 150.00
task #10101 Design and implement a role based access con...	2.00	Co-working space (Hourly)	PHP 200.00
task #10101 Add Status dropdown filter component alongs...	1.00	Co-working space (Hourly)	PHP 100.00
task #10101 Add Category dropdown filter component to s...	1.00	Co-working space (Hourly)	PHP 100.00
task #10101 Export Ockam Materials Only from Material R...	1.00	Co-working space (Hourly)	PHP 100.00
task #10101 Display Upload Date on Materials to Distingue...	1.50	Co-working space (Hourly)	PHP 150.00
task #10101 Implement an activity logging system that reso...	8.00	Co-working space (Hourly)	PHP 800.00
story #10101 As a Librarian Administrator, I want to be...	4.00	Co-working space (Hourly)	PHP 400.00
task #10101 Use OpenProject to update work package stat...	2.00	Co-working space (Hourly)	PHP 200.00
story #10101 As an IT Administrator, I want to define a...	4.00	Co-working space (Hourly)	PHP 400.00
Feature #10101 Feature 10.0 Add monitoring on who edit...	8.00	Co-working space (Hourly)	PHP 800.00



Backlogs

L12 AY 2025-2026 T3 Sprint 02 15 ^		04/22/2026 ~ 05/09/2026	177 points	...
FEATURE #6526	Closed	Feature 12.0 Targeted Dormant Material Export	0 points	...
USER STORY #6702	Closed	As a Librarian Administrator, I want to export a targeted list of dormant materials (not accessed for 1 month) from the LitPath AI dashboard, so that I can review and manage underperforming thesis and dissertation content efficiently.	20 points	...
FEATURE #6527	Closed	Feature 13.0 Least Viewed Metric tracking	0 points	...
USER STORY #6704	Closed	As a Librarian Administrator, I want to view a Least Viewed Materials metric in the Material Rating tab replacing the Top Least Accessed metric, so that I can better track and identify underperforming thesis and dissertation content in LitPath AI.	18 points	...
FEATURE #6514	Closed	Feature 14.0 Query Duration Logging & "Upload Date" Tracking	0 points	...
USER STORY #6604	Closed	As an admin, I want the system to automatically log how long each user stays in a session so that I can monitor user engagement and activity.	23 points	...
USER STORY #6605	Closed	As an admin, I want the upload date of each material to be automatically recorded so that I can track when it was added to the system.	16 points	...
FEATURE #6515	Closed	Feature 15.0 Feedback Filtering Realignment & Advanced Report Filtering	0 points	...
USER STORY #6796	Closed	As a Librarian Administrator, I want to filter feedback records by Category and Status, So that I can quickly isolate specific subsets of feedback data and generate focused reports without manually scanning through unrelated entries.	22 points	...
FEATURE #6516	Closed	Feature 16.0 CSV Export Enhancement and PDF Report Export	0 points	...
USER STORY #6801	Closed	As a Library Administrator, I want to export feedback data to CSV or PDF based on the filters I've applied, so the file only includes the specific data I need and not the entire dataset.	20 points	...
FEATURE #6524	Closed	Feature 17.0 Admin Hierarchy	0 points	...
USER STORY #6640	Closed	As an IT Administrator, I want to define and manage a hierarchy of admin roles (IT Administrator and Librarian Administrator) with specific permissions so that each role can securely and efficiently perform their responsibilities within LitPath AI.	32 points	...
FEATURE #6525	Closed	Feature 18.0 Add monitoring on who edited for tracing and logs user id and actions	0 points	...
USER STORY #6838	Closed	As a Librarian Administrator, I want to track and log who reviews and validates user feedback (including user ID and actions taken) so that we can ensure accountability, trace changes, and maintain transparency.	26 points	...

L13 AY 2025-2026 T3 Sprint 03 3 ^		05/08/2026 ~ 05/22/2026	52 points	...
FEATURE #6521	In progress	Feature 11.0 Cloud and Client-side Deployment	0 points	...
USER STORY #6701	In progress	As an end user, I want the web app to be hosted on the cloud so that I can access it anytime from any browser without installing anything.	26 points	...
USER STORY #6803	In progress	As an admin, I want to access the admin dashboard via browser so that I can manage the system remotely without needing a local setup.	26 points	...



Task Board

Story	New	In Review	In progress	Closed
Sprint Impediments	+			
Closed 6526 Feature 12.0 Targeted Dormant Material Export Tracie Tomon	+			6702 As a Librarian Administrator Tracie Tomon
Closed 6702 As a Librarian Administrator, I want to export a targeted list of dormant materials (not Tracie Tomon 20	+			6703 Export Dormant Materials Tracie Tomon
Closed 6527 Feature 13.0 Least Viewed Metric tracking Tracie Tomon	+			6704 As a Librarian Administrator Tracie Tomon
Closed 6704 As a Librarian Administrator, I want to view a Least Viewed Materials metric in the Tracie Tomon 18	+			6705 Set 1-Month Inactivity Rule for Tracie Tomon 6706 Display Upload Date on Materials Tracie Tomon
Closed 6514 Feature 14.0 Query Duration Logging & "Upload Date" Tracking Joshua Sta Ana	+			6804 As an admin, I want the system to Joshua Sta Ana 6805 As an admin, I want the upload date Joshua Sta Ana

Closed 6804 As an admin, I want the system to automatically log how long each user stays in a Joshua Sta Ana 23	+				6899 Implement User-Session Duration Joshua Sta Ana
Closed 6805 As an admin, I want the upload date of each material to be automatically recorded Joshua Sta Ana 16	+				6900 Automatically Record Upload Date Joshua Sta Ana
Closed 6515 Feature 15.0 Feedback Filtering, Realignment & Advanced Report Filtering Jenine Elaine Dulay	+				6796 As a Librarian Administrator Jenine Elaine Dulay
Closed 6796 As a Librarian Administrator, I want to filter feedback records by Category and Status, So Jenine Elaine Dulay 22	+				6798 Add Status dropdown filter Jenine Elaine Dulay 6799 Add Category dropdown Jenine Elaine Dulay
Closed 6516 Feature 16.0 CSV Export Enhancement and PDF Report Export Jenine Elaine Dulay	+				6801 As a Library Administrator, I want to Jenine Elaine Dulay
Closed 6801 As a Library Administrator, I want to export feedback data to CSV or PDF based on the Jenine Elaine Dulay 20	+				6802 Create CSV export endpoint Jenine Elaine Dulay
Closed 6524 Feature 17.0 Admin Hierarchy Charjoy Cempron	+				6640 As an IT Administrator, I want to Charjoy Cempron

Closed 6640 As an IT Administrator, I want to define and manage a hierarchy of admin roles (IT Charjoy Cempron 32	+				6641 Design and implement a role-based Charjoy Cempron
Closed 6525 Feature 18.0 Add monitoring on who edited for tracing and logs user id and actions Charjoy Cempron	+				6638 As a Librarian Administrator Charjoy Cempron
Closed 6638 As a Librarian Administrator, I want to track and log who reviews and validates user Charjoy Cempron 26	+				6639 Implement an activity logging Charjoy Cempron




Burndown Chart

APC_2025_2026_T1_M0311_06... / Backlogs / 1.12 AY 2025-2026 T3 Sprint 02

1.12 AY 2025-2026 T3 Sprint 02

04/02/2026 - 05/09/2026

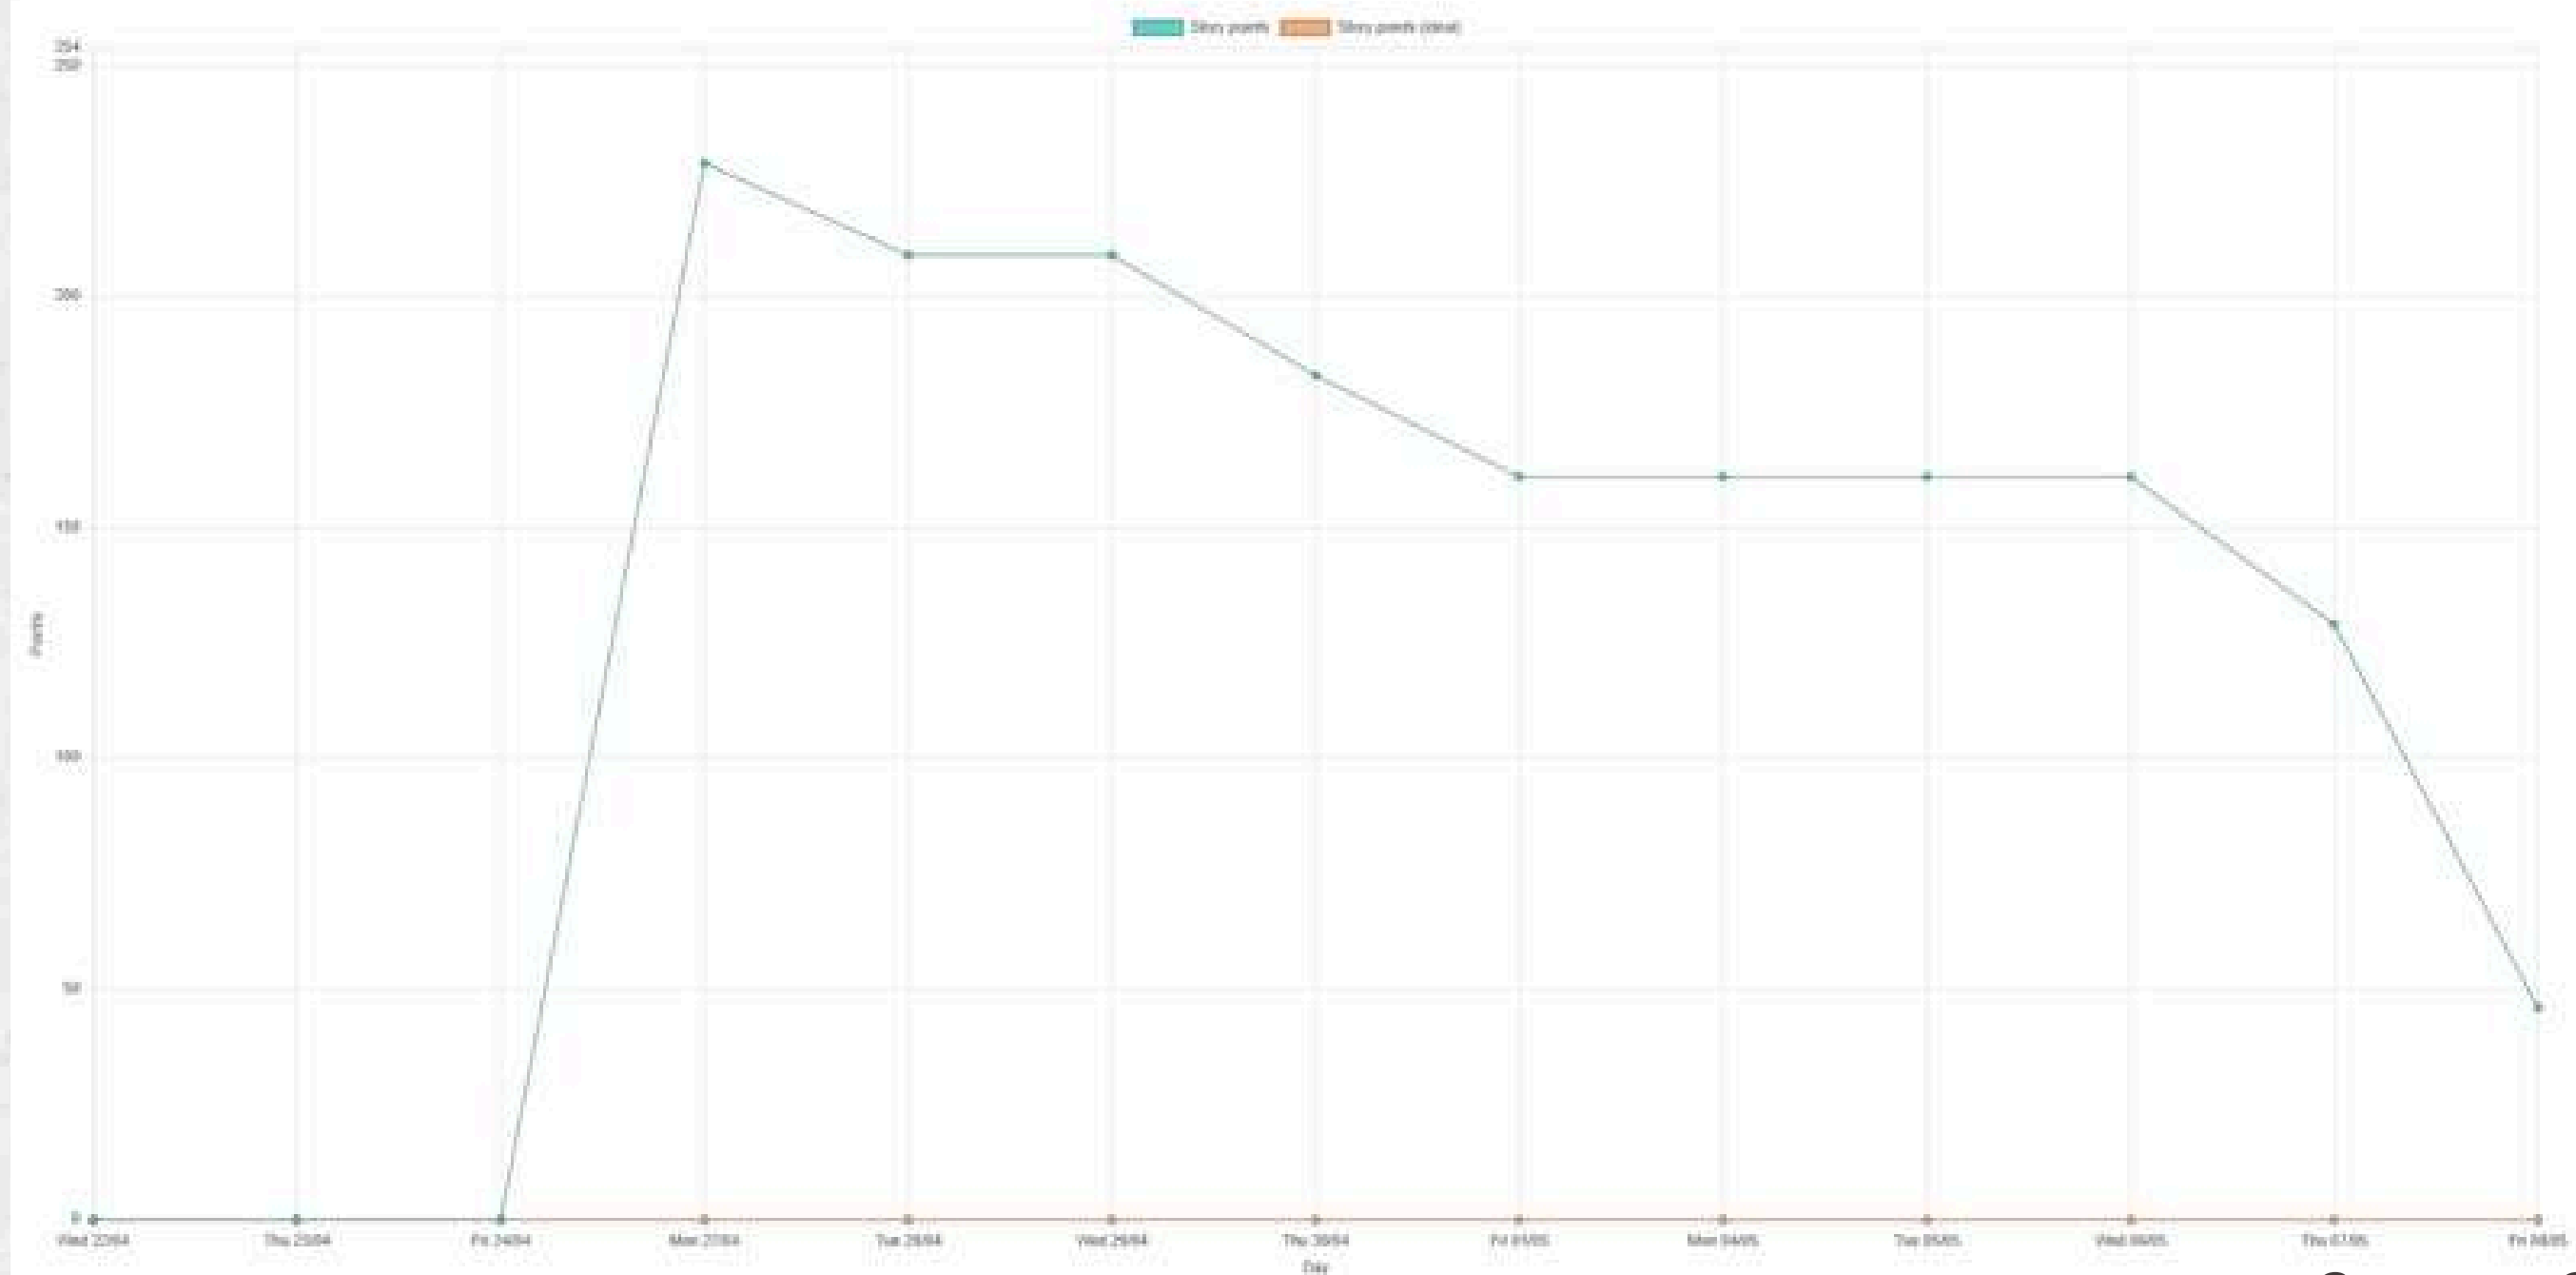

Cempron, Charijoy



Forums

APC_2025_2026_T1_M1231_G0... / Forums / AY 2025-2026 T3 Sprint 02 Dai... / Sprint 2 Week 1 Day 01 Daily ...

Sprint 2 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report (April 24, 2026)UnwatchQuoteEditDelete

Added by Tracie Toman 22 days ago

Answer the following questions:

1. What did you accomplish yesterday?

2. What can I commit today?

3. Anything blocking my progress?

Replies (4)

JD

RE: Sprint 2 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report (April 24, 2026) - Added by Jenine Elaine Dulay 22 days ago

1. What did you accomplish yesterday?

Started implementing the following tasks: setting the welcome page background blur to 55%, adding the NIR region, and updating the Client Type logic (showing School Level and School Name for students, and Company or N/A for citizens).

Changes are not yet committed due to issues when pulling from Git, possibly caused by concurrent commits from others.

2. What can I commit today?

Work on aligning the Sources Information card with the AI Overview section.

3. Anything blocking my progress?

Academic workload from other subjects.

TT

RE: Sprint 2 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report (April 24, 2026) - Added by Tracie Toman 19 days ago

1. What did you accomplish yesterday?

Messaged the project advisers for consultation.

Set up a message on the forum for the DS report.

Created user stories and tasks for each of my assigned backlogs.

Checked and listed the additional documents for finals to be assigned to other members.

2. What can I commit today?

Check the minutes of the meetings sent by Chari.

Sync all files to both SharePoint sites.

Set the budget and cost in OpenProject.

Set up a new filter for the new sprint and assign possible documents to each member.

3. Anything blocking my progress?

Other schoolwork, commitments, and work schedule.

CC

RE: Sprint 2 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report (April 24, 2026) - Added by Charlojy Cempron 19 days ago

1. What did you accomplish yesterday?

I did my pending minutes of the meeting.

2. What can I commit today?

I will do the revisions suggested by the client in account registration and profile.

3. Anything blocking my progress?

I don't have my own laptop or desktop at home.

JA

RE: Sprint 2 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report (April 24, 2026) - Added by Joshua Sta Ana 19 days ago

1. What did you accomplish yesterday?

Reviewed pending project backlogs

Created open project drafts for completion

Code file and code structural refinement review specific to main dashboard to eliminate code errors during development

2. What can I commit today?

To create task, user stories from the official assigned work packages

Watch implementation tutorial for resend.com/a developer-focused email platform designed to build, test, and deliver transactional and email notifications via API

3. Anything blocking my progress?

N/a

APC_2025_2026_T1_M1231_G0... / Forums / AY 2025-2026 T3 Sprint 02 Dai... / Sprint 2 Week 1 Day 02 Daily ...

Sprint 2 Week 1 Day 02 Daily Scrum Meeting Individual Updated Report (April 27, 2026)UnwatchQuoteEditDelete

Added by Tracie Toman 19 days ago

Answer the following questions:

1. What did you accomplish yesterday?

2. What can I commit today?

3. Anything blocking my progress?

Replies (4)

CC

RE: Sprint 2 Week 1 Day 02 Daily Scrum Meeting Individual Updated Report (April 27, 2026) - Added by Charlojy Cempron 19 days ago

1. What did you accomplish yesterday?

I did the revisions suggested by the client in account registration and profile.

2. What can I commit today?

I will start the feature admin hierarchy.

3. Anything blocking my progress?

I don't have my own laptop or desktop at home.

JD

RE: Sprint 2 Week 1 Day 02 Daily Scrum Meeting Individual Updated Report (April 27, 2026) - Added by Jenine Elaine Dulay 19 days ago

1. What did you accomplish yesterday?

I implemented the aligning of the Sources Information card with the AI Overview section. I updated my work packages in openproject with the tasks I was assigned to.

2. What can I commit today?

Work on Feature 16.0 CSV Export Enhancement and PDF Report Export and start add user stories and tasks to the features I was assigned to.

3. Anything blocking my progress?

Academic workload from other subjects.

TT

RE: Sprint 2 Week 1 Day 02 Daily Scrum Meeting Individual Updated Report (April 27, 2026) - Added by Tracie Toman 19 days ago

1. What did you accomplish yesterday?

Set up a new message in the forum.

Checked the minutes and uploaded them to the SharePoint sites.

Synced files across both SharePoint sites.

Uploaded and assigned PM documents in SharePoint.

Prepared for the Backlog Refinement meeting.

2. What can I commit today?

Start working on the assigned documents.

Update the OpenProject budget and add a filter.

3. Anything blocking my progress?

Other schoolwork, commitments, and work schedule.

JA

RE: Sprint 2 Week 1 Day 02 Daily Scrum Meeting Individual Updated Report (April 27, 2026) - Added by Joshua Sta Ana 19 days ago

1. What did you accomplish yesterday?

Worked at Proxmox VE instance maintenance updates, had to checked for new ubuntu server release for possible Lighthouse project migration and feature upgrades for system stability and security focus server environment.

The latest Long Term Support (LTS) version is Ubuntu 26.04 LTS "Resolute Raccoon", released on April 23, 2026. It provides enterprise-grade stability with up to 10-15 years of security maintenance, making it the recommended choice for new production deployments. The prior LTS is 24.04A, with 25.10 being the latest interim release.

Had to checked for new github team commits for commit updates.

2. What can I commit today?

To Re-watch recordings of DS-W1-Q2 for review

To Work with pending work packages to finish Task in accordance with assigned user stories and filterview hierarchy refined for organization.

To start with code file refinement and optimization prior developing assigned new features

To continue implementing email notification as feature development

To start working on the assigned PMBOK Documents

3. Anything blocking my progress?

N/a

APC_2025_2026_T1_M1231_G0... / Forums / AY 2025-2026 T3 Sprint 02 Dai... / Sprint 2 Week 1 Day 03 Daily ...

Sprint 2 Week 1 Day 03 Daily Scrum Meeting Individual Updated Report (April 28, 2026)UnwatchQuoteEditDelete

Added by Jenine Elaine Dulay 18 days ago

Answer the following questions:

1. What did you accomplish yesterday?

2. What can I commit today?

3. Anything blocking my progress?

Replies (4)

JD

RE: Sprint 2 Week 1 Day 03 Daily Scrum Meeting Individual Updated Report (April 28, 2026) - Added by Jenine Elaine Dulay 18 days ago

1. What did you accomplish yesterday?

I combined the export functionality into a single button with a dropdown in the Overview tab. I also completed Feature 16.0 (CSV Export Enhancement and PDF Report Export). Additionally, I updated the related work packages to reflect the development progress. I'll continue refining the feature.

2. What can I commit today?

Start working on the Business Model Canvas and the Requirements Management Plan.

3. Anything blocking my progress?

Academic workload from other subjects.

JA

RE: Sprint 2 Week 1 Day 03 Daily Scrum Meeting Individual Updated Report (April 28, 2026) - Added by Joshua Sta Ana 18 days ago

1. What did you accomplish yesterday?

Performed open project work packages organization and completed the lacking of task and sub-tasks per my assigned user stories.

2. What can I commit today?

To start working and completing on the PMBOK assigned document specific to Configuration Management Plan.

Started code file structural refinement for continuation tonight.

Continuation Review of Cloudflare and Proxmox VE integration documentations

3. Anything blocking my progress?

CC

RE: Sprint 2 Week 1 Day 03 Daily Scrum Meeting Individual Updated Report (April 28, 2026) - Added by Charlojy Cempron 18 days ago

1. What did you accomplish yesterday?

I started the feature admin hierarchy.

2. What can I commit today?

I will continue the feature and start doing the PMBOK document assigned to me.

3. Anything blocking my progress?

I don't have my own laptop or desktop at home and other subjects.

TT

RE: Sprint 2 Week 1 Day 03 Daily Scrum Meeting Individual Updated Report (April 28, 2026) - Added by Tracie Toman 17 days ago

1. What did you accomplish yesterday?

Started working on the assigned documents for the 01 Initiation phase.

2. What can I commit today?

Schedule a meeting with the advisers for consultation. Finish the 01 and 02 phase documents to be reviewed with the advisers. Post another message in the forum for Week 2 DS.

3. Anything blocking my progress?

Other schoolwork, commitments, and work schedule.



DEMO

Individual Contributions



Cempron, Charijoy

DOCUMENTATION:

- 02 - Risk Management Plan
- 02 - Risk Register
- 05 - Transition Out Plan



DOCUMENTATION:

- 02 - Configuration Management Plan
- 04 - Project Status Report



Dulay, Jenine Elaine

DOCUMENTATION:

- 01 - Business Model Canvas
- 02 - Requirements Management Plan
- 05 - Post-Project Review



DOCUMENTATION:

- 01 - Feasibility Study
- 02 - Change Management Plan
- 05 - Project Acceptance
- 05 - Lessons Learned

Dulay, Jenine Elaine



**THANK
YOU!**
